

# **La Crosse Center Expansion & Renovation**

**Monthly Summary: December 2019**

**La Crosse, Wisconsin**

ISG



**KRAUS-ANDERSON®**  
*Construction Company*



December 31<sup>st</sup>, 2019

As we conclude the month of December and start working into January, this report details some of the major site activities completed through this month. There is also a brief list showing the activities we will have ongoing in the month of January. Attached are the overall project schedule and two graphs representing labor statistics for the month of December.


Work in progress and completed in December:

- Site fencing, barricades, and signage installed
- Entrance Hall interior temporary wall constructed
- Entrance Hall exterior slab sawcut and removed
- Entrance Hall footing/foundation ground thawed, excavated, poured, and backfilled
- Entrance Hall CFM wall constructed and temporary frames relocated
- West side storm/sanitary sewer ground thawed, excavated, installed, and backfilled
- Ballroom column pad footings ground thawed, excavated, and poured (ongoing)

Upcoming Work in January:

- Front Street shutdown
- Entrance Hall stoop, sidewalk, and interior/exterior slab pour
- Entrance Hall CFM wall rough in, interior/exterior finish install, and electrical finish install
- Entrance Hall temporary door/hardware install and turnover to LCC
- Ballroom column pad footings ground thaw, excavation, and pour (ongoing)
- Ballroom column bases pour and backfill


LCC Expansion  
DD Project Schedule

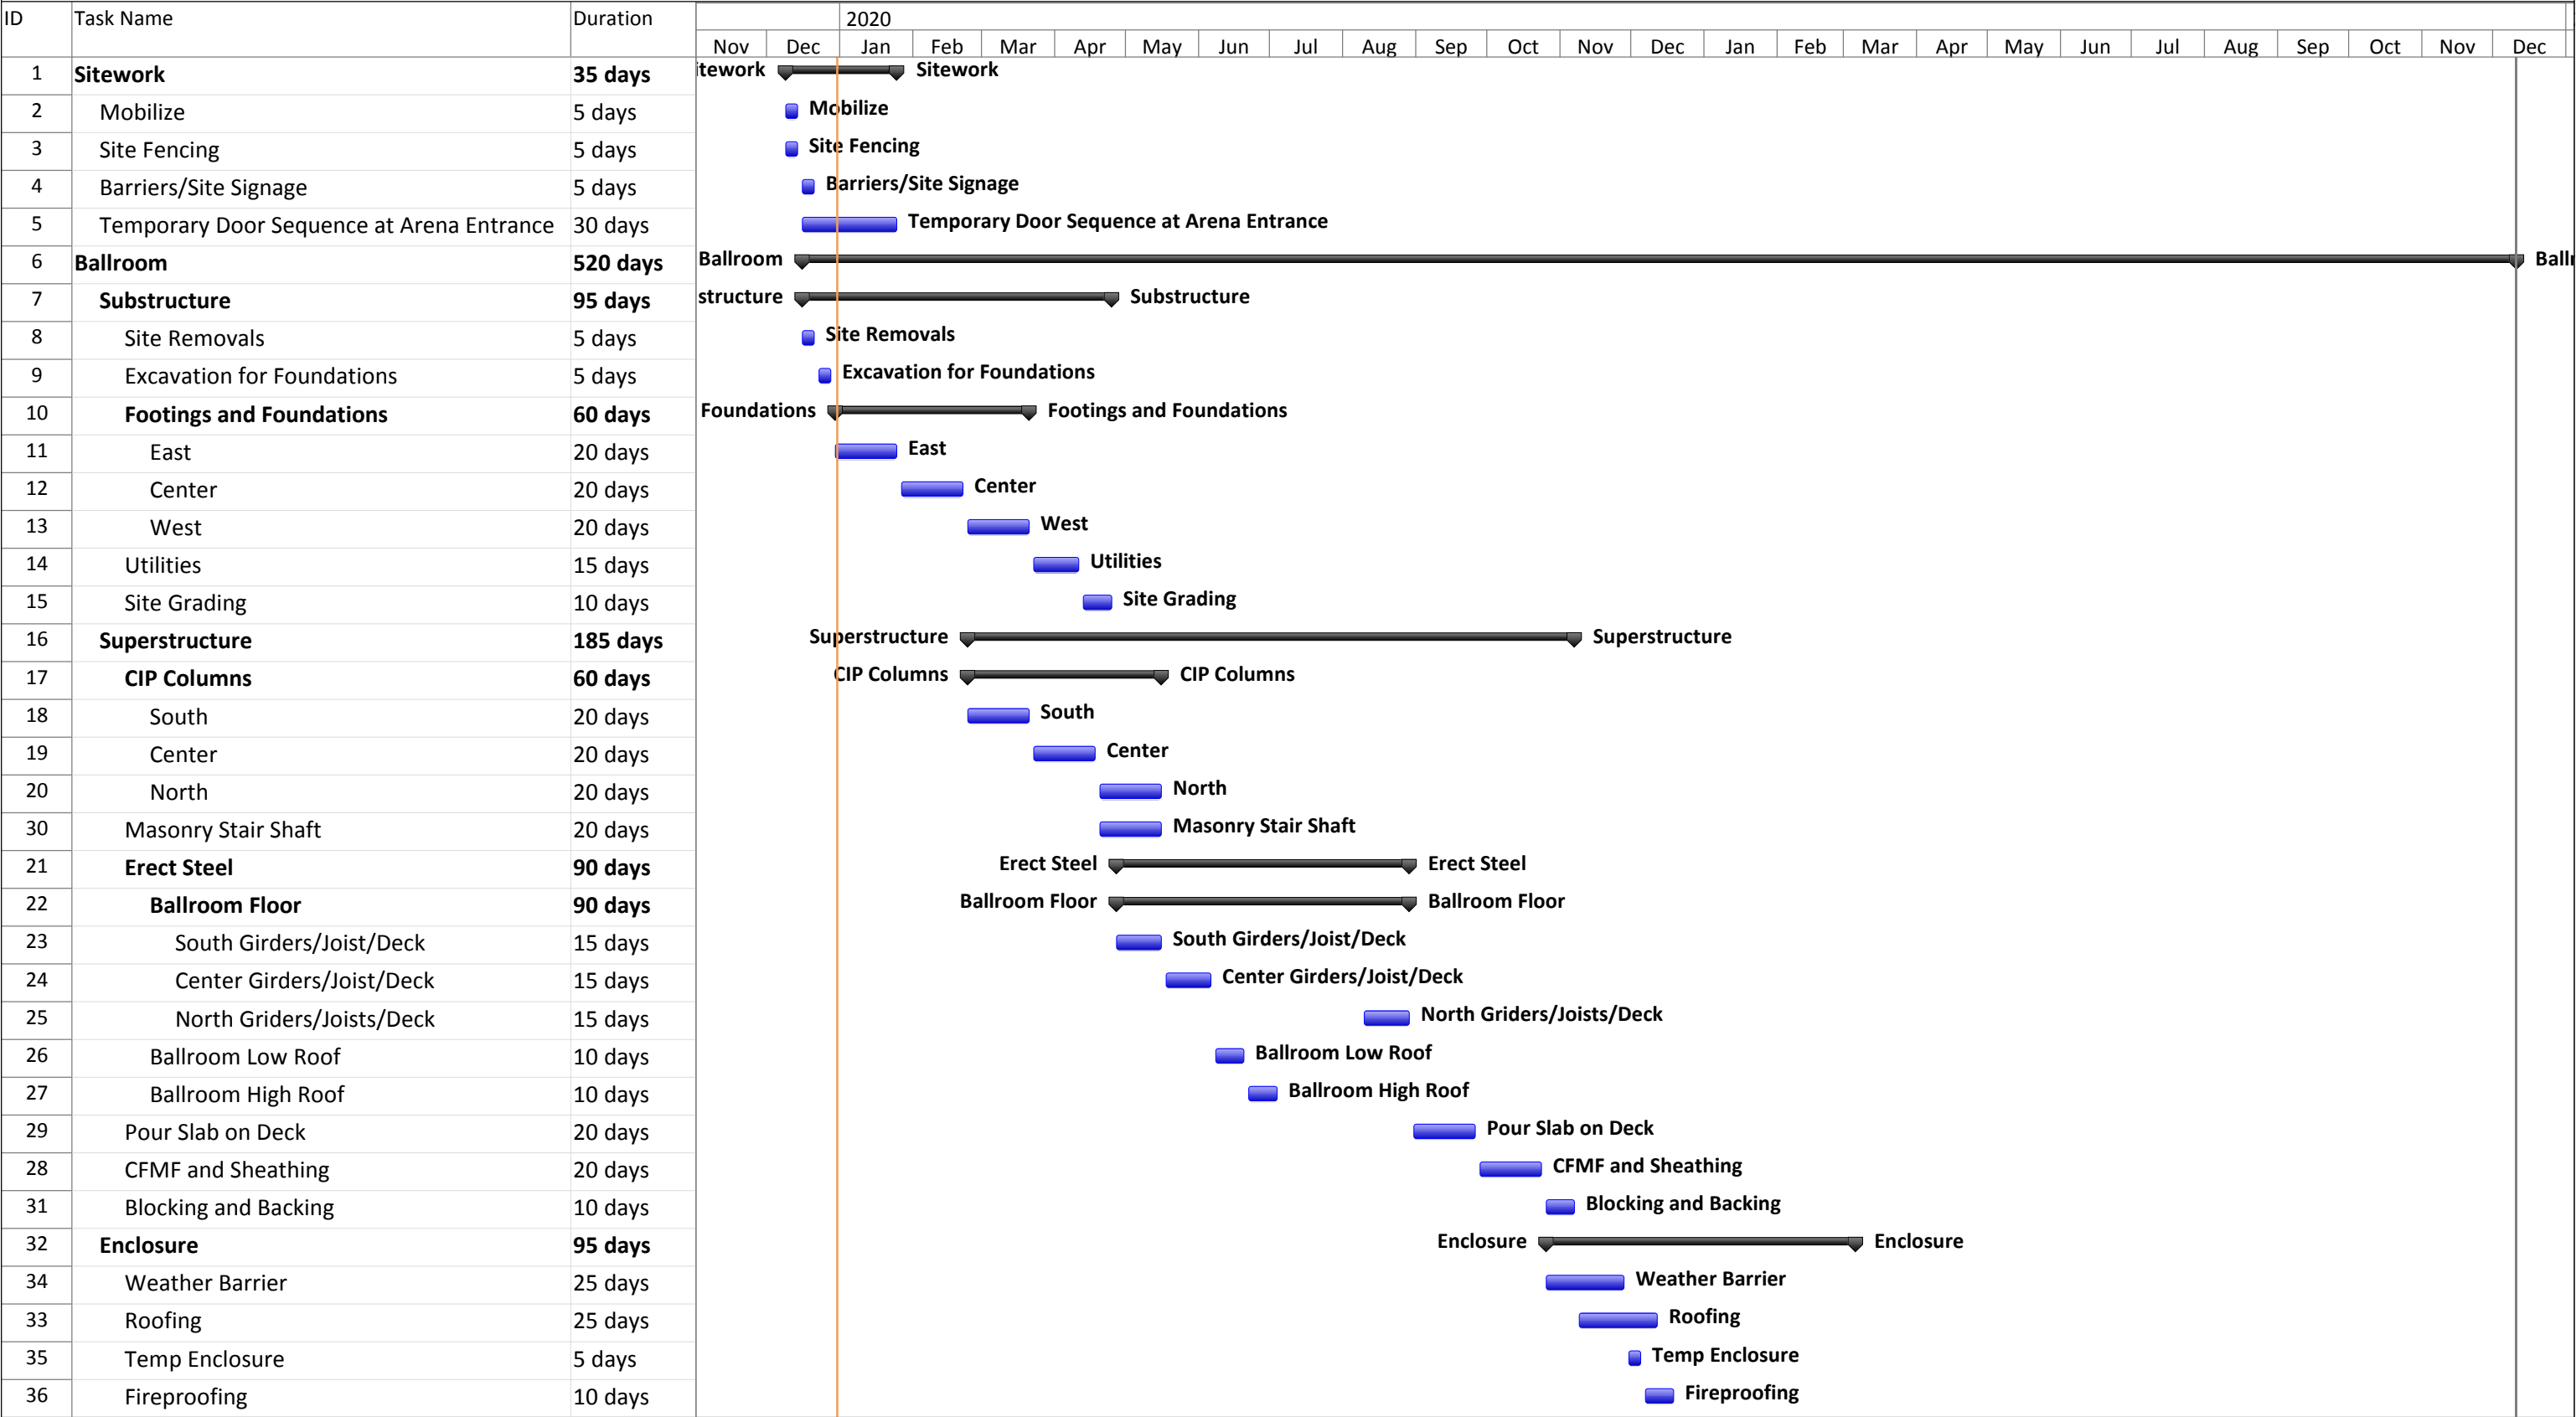


## LCC Expansion DD Project Schedule

ID	Task Name	Duration	2020																											
			Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
37	Glass and Glazing	40 days	<div><div></div><div>Glass and Glazing</div></div>																											
38	Metal Panel	25 days	<div><div></div><div>Metal Panel</div></div>																											
39	Interior	220 days	<div><div>Interior</div><div></div><div>Interior</div></div>																											
40	Studs	40 days	<div><div></div><div>Studs</div></div>																											
41	Finishes	180 days	<div><div></div><div>Finishes</div></div>																											
42	Inspection and Turnover	35 days	<div><div></div><div>Inspe</div></div>																											
61	Exhibit/Entrance Hall (North Hall)	256 days	<div><div>Exhibit/Entrance Hall (North Hall)</div><div></div><div>Exhibit/Entrance Hall (North Hall)</div></div>																											
62	Prep and Demo	45 days	<div><div>Prep and Demo</div><div></div><div>Prep and Demo</div></div>																											
64	Temporary Barriers	15 days	<div><div></div><div>Temporary Barriers</div></div>																											
63	Selective Demolition	10 days	<div><div></div><div>Selective Demolition</div></div>																											
65	Shoring For Radisson Connector	10 days	<div><div></div><div>Shoring For Radisson Connector</div></div>																											
66	North Hall Closes	0 days	<div><div>3/2</div><div>North Hall Closes</div></div>																											
67	Building Demolition	20 days	<div><div></div><div>Building Demolition</div></div>																											
68	Substructure	40 days	<div><div>Substructure</div><div></div><div>Substructure</div></div>																											
69	Perimeter Footing Ex	5 days	<div><div></div><div>Perimeter Footing Ex</div></div>																											
70	FPS Perimeter Foundations	15 days	<div><div></div><div>FPS Perimeter Foundations</div></div>																											
71	FPS Retaining Wall	10 days	<div><div></div><div>FPS Retaining Wall</div></div>																											
72	FPS Column Pads	10 days	<div><div></div><div>FPS Column Pads</div></div>																											
73	Superstructure	100 days	<div><div>Superstructure</div><div></div><div>Superstructure</div></div>																											
76	Elevator/Stair Shaft	20 days	<div><div></div><div>Elevator/Stair Shaft</div></div>																											
74	Erect Precast	10 days	<div><div></div><div>Erect Precast</div></div>																											
75	Erect Steel Exhibit Hall Roof	15 days	<div><div></div><div>Erect Steel Exhibit Hall Roof</div></div>																											
77	Masonry Infill	15 days	<div><div></div><div>Masonry Infill</div></div>																											
79	In Ground MEP's	10 days	<div><div></div><div>In Ground MEP's</div></div>																											
80	Pour Slab on Grade	10 days	<div><div></div><div>Pour Slab on Grade</div></div>																											
78	Pour Ramp Slab	10 days	<div><div></div><div>Pour Ramp Slab</div></div>																											
86	Ballroom Level Construction	75 days	<div><div>Ballroom Level Construction</div><div></div><div>Ballroom Level Construction</div></div>																											
87	Erect Steel	20 days	<div><div></div><div>Erect Steel</div></div>																											
89	Pour Ballroom Level Slab	10 days	<div><div></div><div>Pour Ballroom Level Slab</div></div>																											
90	CFMF	10 days	<div><div></div><div>CFMF</div></div>																											
88	Pour 4th FL Slab	5 days	<div><div></div><div>Pour 4th FL Slab</div></div>																											
91	Exterior Blocking	10 days	<div><div></div><div>Exterior Blocking</div></div>																											
92	Weather Barrier	10 days	<div><div></div><div>Weather Barrier</div></div>																											
93	Roofing 6K SF	10 days	<div><div></div><div>Roofing 6K SF</div></div>																											
94	Curtain Wall	15 days	<div><div></div><div>Curtain Wall</div></div>																											
95	Interiors	80 days	<div><div>Interiors</div><div></div><div>Interiors</div></div>																											

LCC Expansion  
DD Project Schedule

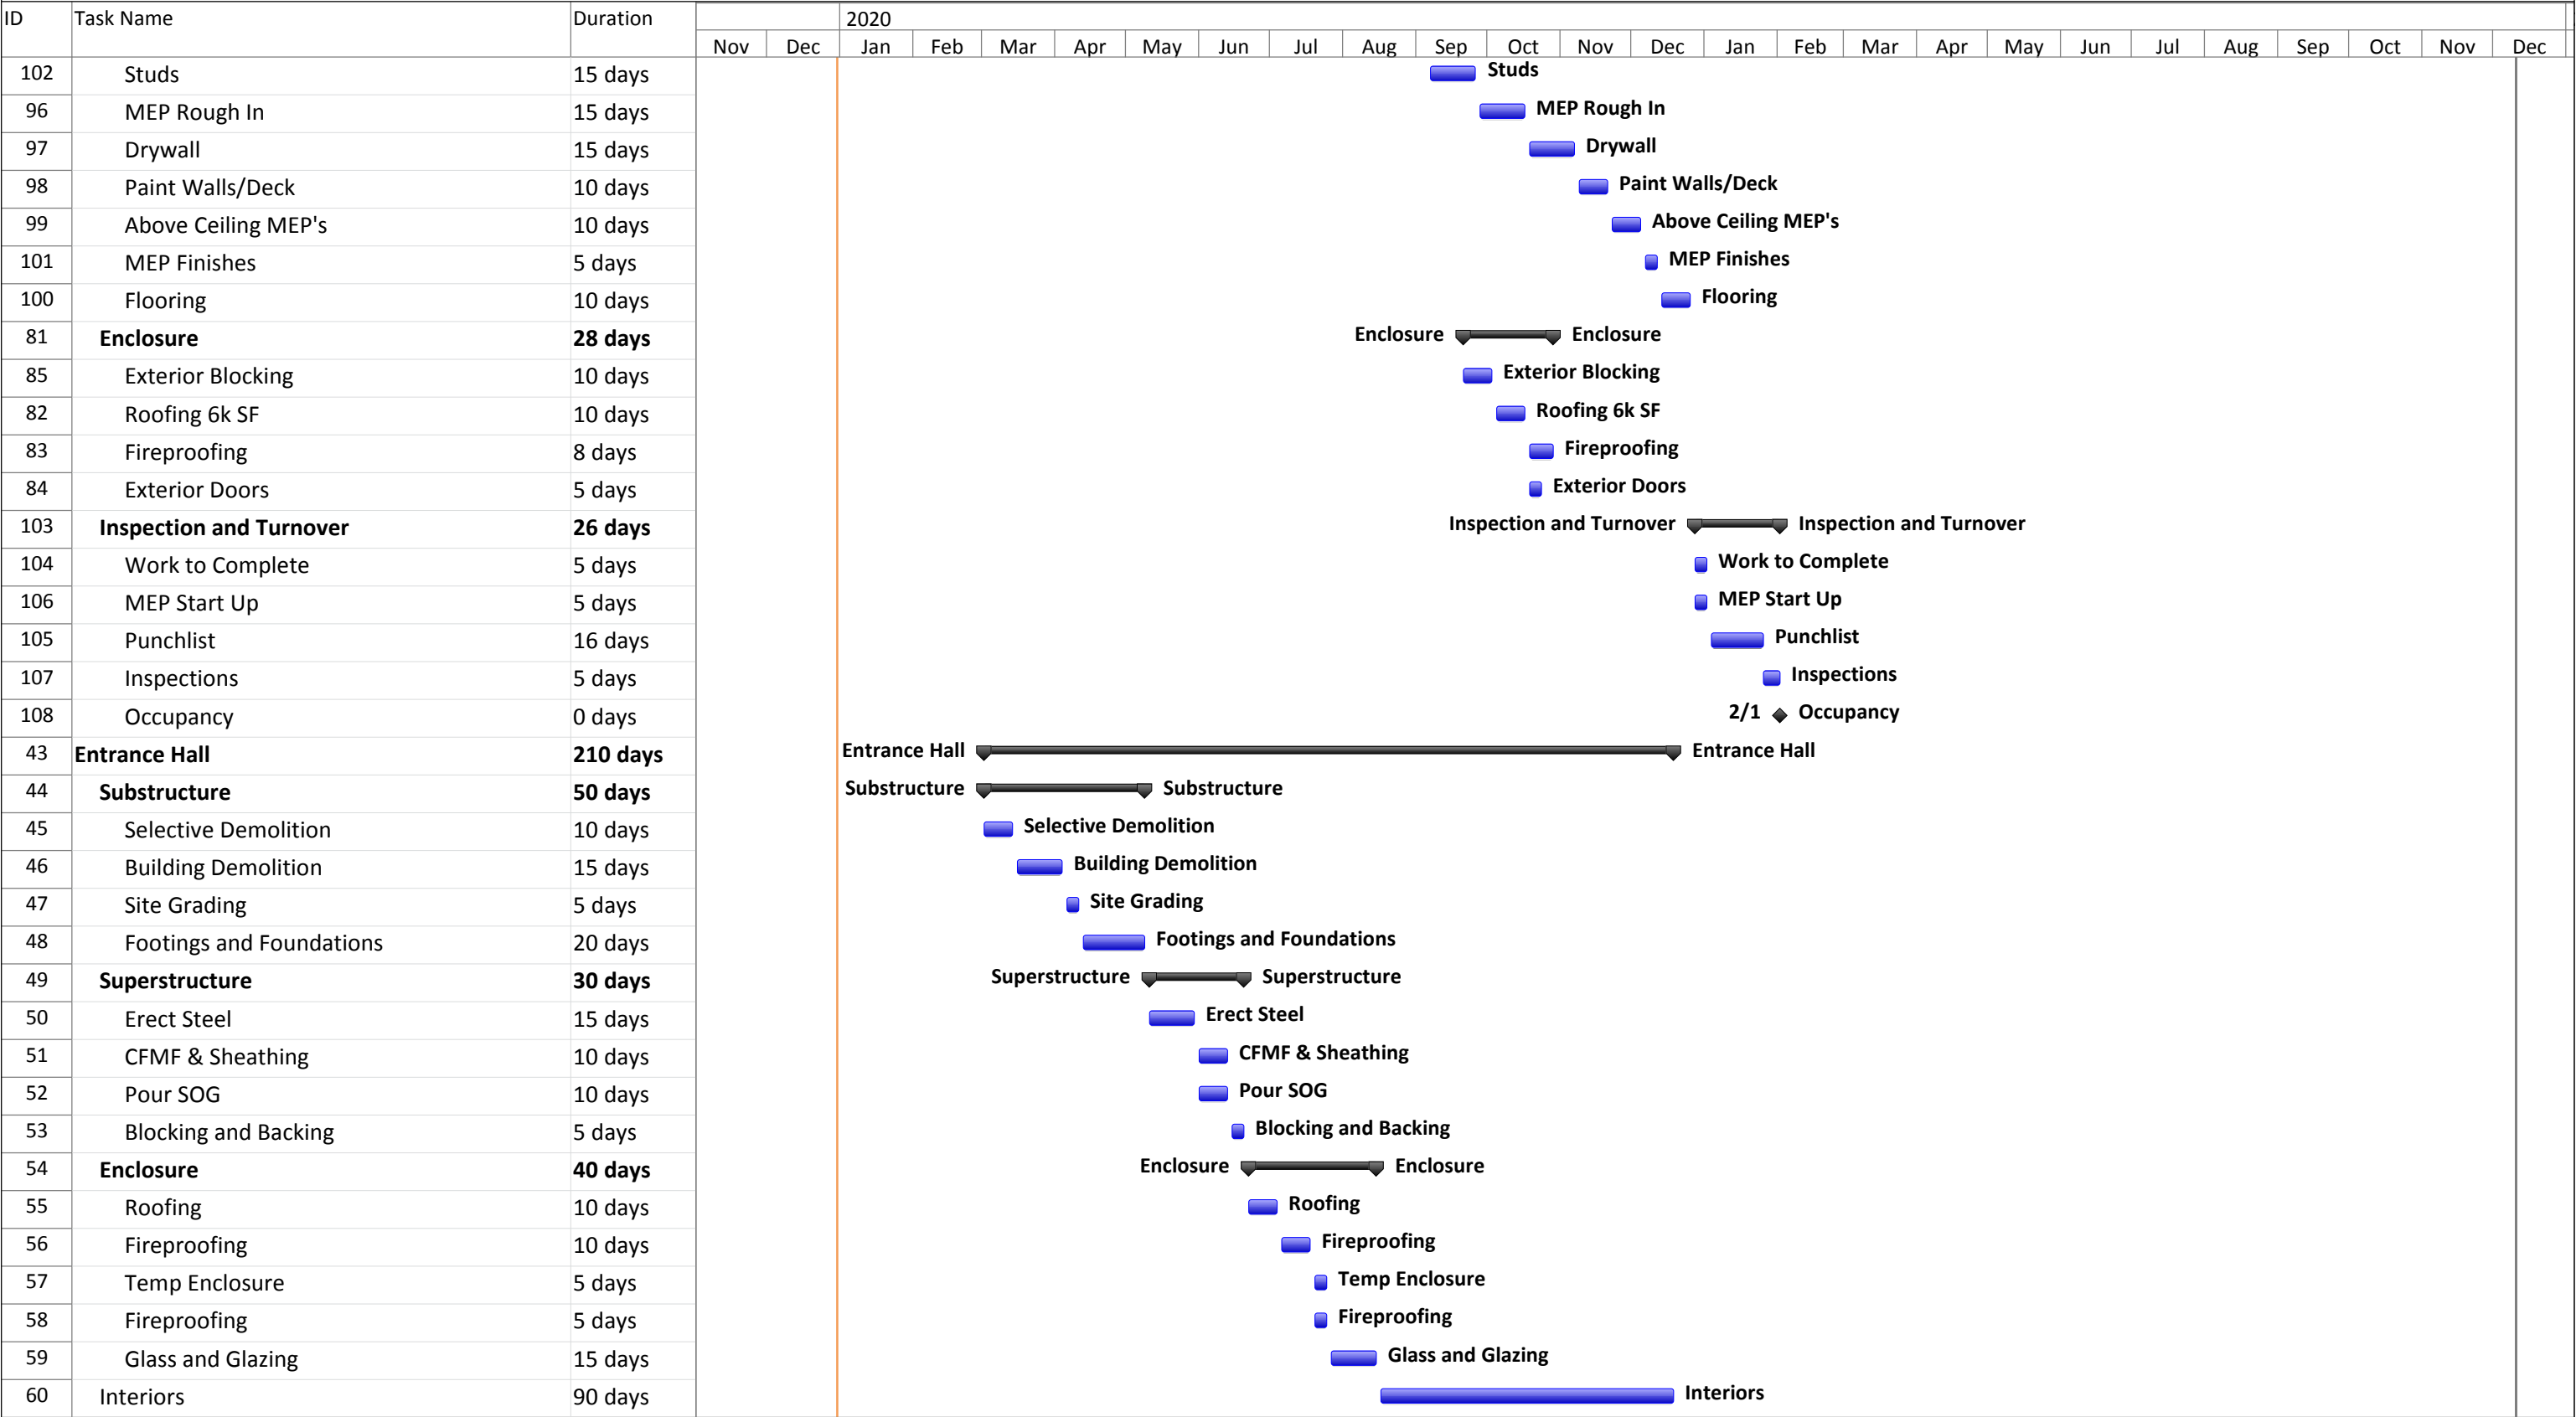

## La Crosse Center Expansion & Renovation

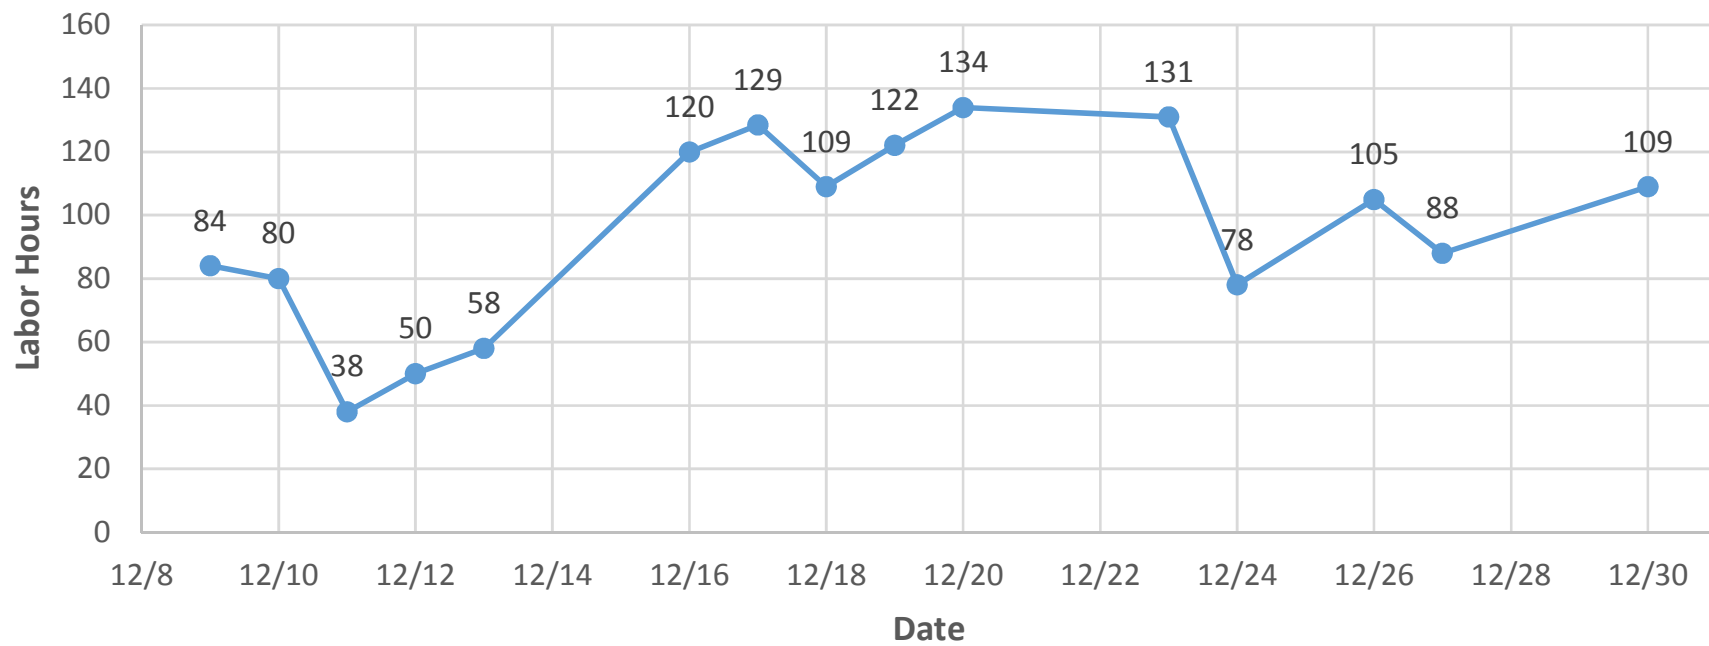

## La Crosse Center Expansion & Renovation

