

**FOREST HILLS
CONSTRUCTION SCHEDULE**

ID	Task Name	Duration	Start	Finish
1	Mobilization	15 days	Mon 6/15/15	Fri 7/3/15
2	Cleaning 13, 14, 18 tree	13 days	Thu 6/25/15	Mon 7/13/15
3	18 Green, 10 Tee, 18 tee	25 days	Mon 6/29/15	Fri 7/31/15
4	Earthwork	7 days	Mon 6/29/15	Tue 7/17/15
5	Shopping	5 days	Mon 7/6/15	Fri 7/10/15
6	Drillhole	3 days	Fri 7/10/15	Tue 7/14/15
7	Green Construction	3 days	Wed 7/15/15	Fri 7/17/15
8	Intgation	3 days	Mon 7/20/15	Wed 7/22/15
9	Cart Path Construction	3 days	Mon 7/27/15	Wed 7/29/15
10	Bunker Construction	1 day	Mon 7/27/15	Mon 7/27/15
11	Grossing	4 days	Tue 7/28/15	Fri 7/31/15
12	13, 14, 15	46 days	Tue 7/14/15	Tue 9/15/15
13	Cleatfing #15	3 days	Tue 7/14/15	Thu 7/16/15
14	Stlp Topscell 13, 14	3 days	Tue 7/14/15	Thu 7/16/15
15	Earthwork 13, 14	5 days	Fri 7/17/15	Thu 7/23/15
16	Shopping - Hole 13	4 days	Fri 7/24/15	Wed 7/29/15
17	Drainage - Hole 13	3 days	Mon 8/3/15	Wed 8/5/15
18	Green Construction - #13	2 days	Wed 8/5/15	Thu 8/6/15
19	Intgation - hole 13	3 days	Fri 8/7/15	Tue 8/11/15
20	Earthwork - hole 15	4 days	Mon 8/10/15	Thu 8/13/15
21	Shopping - Hole 14, 15	4 days	Fri 8/14/15	Wed 8/19/15
22	Drainage - Hole 14	3 days	Thu 8/20/15	Mon 8/24/15
23	Green Construction - #14	3 days	Tue 8/25/15	Thu 8/27/15
24	Intgation - hole 14, 15	5 days	Thu 8/27/15	Wed 9/2/15
25	Cart Path Construction	3 days	Thu 9/3/15	Mon 9/7/15
26	Bunker Construction	2 days	Mon 9/7/15	Tue 9/8/15
27	Grossing 13, 14, 15	6 days	Tue 9/8/15	Tue 9/15/15
28	FINAL ADJUSTMENTS / PUNCHLIST	5 days	Fri 9/16/15	Thu 9/22/15



Task
Progress
Milestone

Summary
Rolled Up Task
Rolled Up Milestone


Rolled Up Progress
Split
External Tasks

Project Summary
Group By Summary
Deadline

15-0728

FOREST HILLS GOLF COURSE

LA CROSSE, WISCONSIN

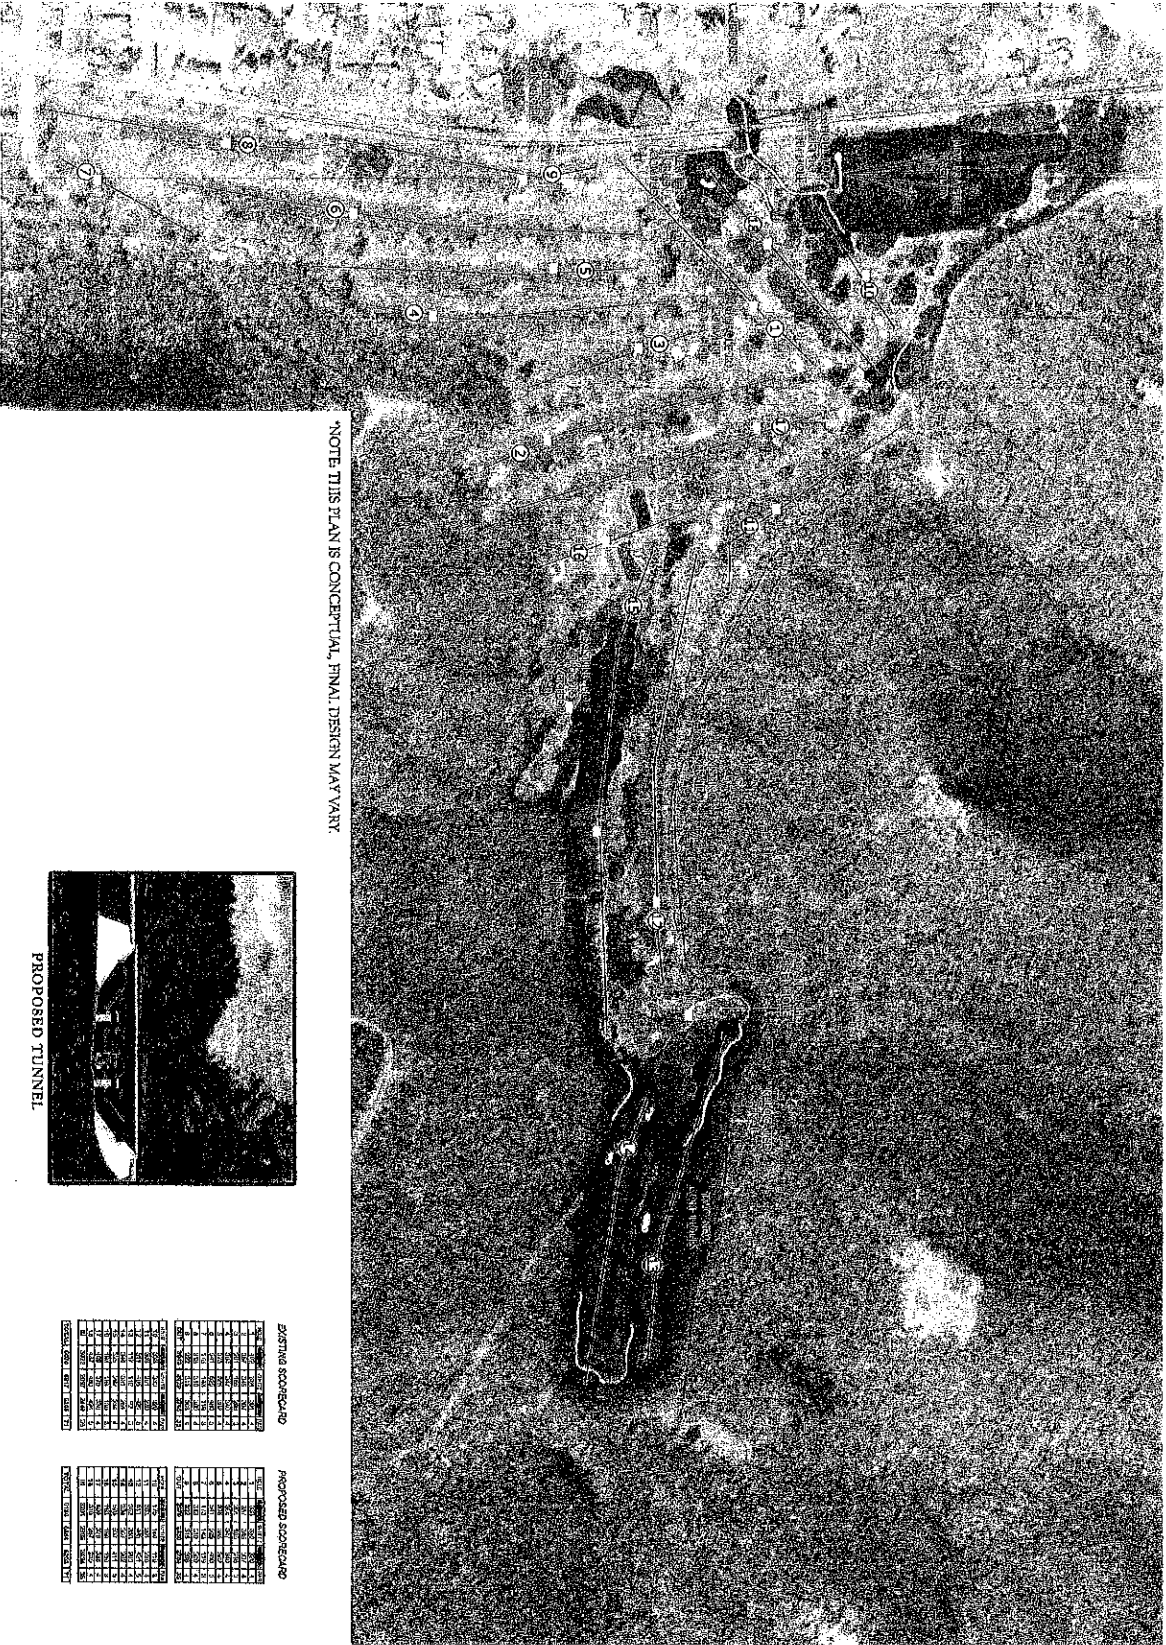

NOTE: THIS PLAN IS CONCEPTUAL, FINAL DESIGN MAY VARY.



PROPOSED TUNNEL

EXISTING SCORECARD

HOLE	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	TOTAL
PAR	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	72
YARDS	350	370	390	410	430	450	470	490	510	530	550	570	590	610	630	650	670	690	4700
GRASS	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	1000
WOODS	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	1000
OBSTACLES	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	1000

PROPOSED SCORECARD

HOLE	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	TOTAL
PAR	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	72
YARDS	350	370	390	410	430	450	470	490	510	530	550	570	590	610	630	650	670	690	4700
GRASS	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	1000
WOODS	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	1000
OBSTACLES	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	100	1000



GOLF COURSE IMPROVEMENTS PLAN

FEBRUARY 25, 2015

