

**CONTRACT CHANGE ORDER**

No. 5

Date Feb. 16, 2018

EDF # 16-021

Contract No. BLDG-2017-18 for the following public work: Fire Storage Building - Training Grounds

between Brickle Brothers Inc. and the City of La Crosse, dated March 9, 2017, is hereby changed in the following particulars, to-wit:

The following specific work is hereby eliminated from such contract:

PR No. 31 - Delete painting of fire suppression piping  
DELETE \$ 800.00

The following specific work is hereby added to such contract:

PR No. 2 - Add second door to the shower area and add sink  
ADD \$ 6,598.12

PR No. 12 - Additional paving work in Green Bay Street  
ADD \$ 4,354.46

PR No. 13 - Add reinforcing steel for concrete approach slab  
ADD \$ 583.00

PR No. 20 - Regrade and pave the Fire Station parking lot  
ADD \$ 13,000.00

PR No. 22 - Saw additional control joints  
ADD \$ 392.00

PR No. 23 - Paint door for shower room  
ADD \$ 210.00

PR No. 26 - Additional caulking for the additional control joints  
ADD \$ 420.00

PR No. 27 - Extra piping to relocate water heater  
ADD \$ 595.58

PR No. 29 - Change shower floor base finish by 90 degrees  
ADD \$ 183.75

PR No. 30 - Furnish and install 2 pipe bollards at propane tanks  
ADD \$ 1,619.40

By virtue of such changes in the contract, the following revisions shall be made in the contract price:

Contract Price -----	\$ 633,802.25
Contract price decreased by eliminations -----	\$ 800.00
Contract price increased by additions-----	\$ 27,956.31
Net Additions -----	\$ 27,156.31
Revised Contract Price -----	\$ 660,958.56

Pet Riv 2/21/18  
**CONTRACTOR**

**APPROVED BY BOARD OF PUBLIC WORKS**

I HEREBY CERTIFY that there are sufficient funds in the treasury to meet the liability assumed by the foregoing addenda to contract, or that provision has been made to pay the liability that will accrue thereunder. (WS 62.15-12; 62.09-10-f)

\_\_\_\_\_  
Controller



\* Updated to display new amount after removing tax from 7 Rivers Mechanical quote for this PR #2

**EJB**

**Proposal Request #2**

**Project:** La Crosse Fire Department Storage Facility

**Owner:** City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

**Contractor:** Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669


The following is a proposal for changes regarding PR #2:


Item #1:	Proposal	
Brickl Bros.	\$ 911.32	
Valley Builders Hardware Company Inc.	\$ 2,459.00	
Bahr Electric	\$ 515.00	
7 Rivers Mechanical	\$ <del>2,522.00</del>	\$2442.00
<hr/>		
Subcontractor Markup:	\$ -274.80	\$270.80
Item #1 Total Proposal:	\$ <del>6,682.42</del>	\$6598.12

New Substantial Completion Date Due to Changes Resulting From this PR: 11/6/2017

New Turnover Date Due to Changes Resulting from this PR: 11/20/2017

**EJB**

CONTRACTOR:  10-5-17  
Ethan Giese Brickl Bros., Inc. Date

OWNER REP:  10-5-17



**Back-Up: PR #2**  
**Project: La Crosse Fire Department Storage Facility**  
**Job #: 7605**  
**Date: 9-28-17**

**Item 1: PR #2**

**Divisions: 03 and 06**

Description: Labor and material to install an Interior Door in the Shower Area.

Labor: \$528  
Material: \$300.47  
Markup (10%): \$82.85

Brickl Bros. Inc, proposes to furnish materials, labor and equipment in accordance with the above specifications, for the sum of:

\$911.32  
Nine Hundred Eleven and 32/100 Dollars

Authorized Signature: \_\_\_\_\_

  
Ethan Giese-Project Supervisor

Date: 10-5-17



**Valley Builders Hardware Company, Inc.**

1527 International Dr, Eau Claire, WI 54701 Phone: (715) 834-1256 Fax: (715) 834-7962

On The Web at: [www.vbhci.com](http://www.vbhci.com)

**Q u o t a t i o n**

Date : 09/21/17

Project : Fire Storage Building

Location : La Crosse, WI

Construction Bulletin: #8

**We Propose to Furnish the Following Materials:**

Add opening #102A. Includes FRP door, frame and hardware.....Add \$2,459.00

**Original Cost : \$4,606.00**

**Add / Deduct Cost : \$2,459.00**

**New Total Cost : \$7,065.00**

sales tax calculated at : 0 percent

Submitted By : Joshua Hartwig

Joshua Hartwig

PRICES ARE BASED ON VALLEY BUILDERS HARDWARE CO., INC. STANDARD TERMS & CONDITIONS. VBHCI STANDARD CERTIFICATE OF LIABILITY INSURANCE AND LIMITS APPLY TO THIS QUOTE. ANY ADDITIONAL COVERAGE REQUIRED WILL BE AT AN ADDITIONAL COST. PRICES FIRM FOR 60 DAYS AND SUBJECT TO STANDARD TERMS. PRICES BASED ON STANDARD FACTORY LEAD TIMES.

SHOULD THERE BE A QUESTION OR CONCERN, PLEASE CALL (715) 834-1256 OR FAX (715) 834-7962.

# Bahr Electric, LLC

# Proposal

Post Office Box 24, West Salem, WI 54669 608-786-1804  
 FAX 608-786-1060

Proposal Submitted To: BRICKL BROS ATTENTION; ETHIAN GIESE		Phone: (608) 786-0890	Date: 09-27-17
Street: 400 BRICKL ROAD		Job Name: LACROSSE FIRE DEPT. STORAGE BUILDING	
City, State and Zip Code: LACROSSE WI, 54601		Job Location: FIRE STATION #3	
Architect: ISG	Date of Plans: 2-10-17	Page: 1 of 1 Pages	Job Phone:

We hereby propose to furnish materials and labor necessary for the completion of

PER YOUR REQUEST, THE FOLLOWING PROPOSAL IS FOR THE INSTALLATION OF ONE 3 WAY SWITCH AND TO RELOCATE PANEL P1. PROPOSAL IS BASED OFF INFORMATION RECEIVED FROM BRICKL BROS. ON 09-20-17, PROPOSAL REQUEST #082

**INCLUSIONS;**

- 1-ADD 3 WAY SWITCH AT SHOWER LOCATION
- 1-RELOCATE PANEL P1 TO ACCOMMODATE THE NEW DOOR

PROPOSAL; \$515.00 (FIVE HUNDRED FIFTEEN DOLLARS AND NO CENTS)

WE PROPOSE hereby to furnish material and labor - complete in accordance with the above specifications, for the sum of:		\$ NOTED ABOVE
Payment to be made as follows: PROGRESS PAYMENTS WITH FINAL PAYMENT DUE UPON COMPLETION		
All material is guaranteed to be as specified. All work to be completed in a substantial workmanlike manner according to specifications submitted, per standard practices. Any alteration or deviation fro above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingent upon strikes, accidents or delays beyond our control. Owner is to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workmen's Compensation Insurance.		
Authorized Signature:	Note: This proposal may be withdrawn by us if not accepted within 30 days.	
ACCEPTANCE OF PROPOSAL The above prices, specifications and conditions are satisfactory and are hereby accepted. You are authorized to do the work as specified. Payment will be made as outlined above.		
	Signature _____	
Date of acceptance:	Signature _____	

# *Z Rivers* MECHANICAL, LLC

187 1<sup>st</sup> St N Suite 2  
La Crescent MN 55947

Phone 608-799-5161 Fax 608-406-2615

Brickl Brothers

September 14, 2017

Re: La Crosse Fire Storage  
Owners request to add a sink. REVISED 10/12/2017 FOR NO TAX

At the meeting today the owner asked that a sink be added to the wall where the current stacked residential wash machine is to be located.

They asked that the sink be the same as the one we installed at Fire Station 1 a couple of years ago.

This sink submittal is attached along with the vendor quote.

Please note the vendor quote is missing the approx. 100.00 freight that will need to be paid on the delivery. The quote shows the same faucet and drain as the existing sink at Fire Station 1.

Materials	85.49
Fixtures	1,236.71
Use tax	0.00
Frts	100.00
Labor 10.62 hours at 73.00	775.63
Profit	244.20
Total	2,442.00

**This is time sensitive as if the engineers review requires additional drain piping to be below the floor this will need to be installed almost immediately.**

We are including a plan page PDF where we show the sink but also note the wash machine will need to be moved to the left.

Beyond approval of this change order we will need documentation that the washer is to be moved and clear understanding of the placement for our washer water and drain installation BUT ALSO the electrician's washer and dryer power supply and the dryer exhaust for the HVAC contractor.

Respectfully Submitted,

John Radecki

Residential

Plumbing, Sewer and Drain Cleaning, Repairs and Service, Water Conditioning

Commercial



**Proposal Request 12 - REVISED 2/9/18 PR**

REJECTED

Project: La Crosse Fire Department Storage Facility

Owner: City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

The following is a proposal for changes regarding PR 12:

	Proposal	
Item #1: Additional Asphalt Paving required, street closure, and painting of Heavy Duty Asphaltic Pavment Patch in Green Bay Street.		
Fahrner Asphalt Sealers, LLC	\$ 250.00	250.00
Central State Signing, Inc.	\$ -1,800.00	40 P.R.
Mathy Construction	\$ 5,591.00	5,591.00
Subcontractor Markup:	\$ -382.05	9,584.00
Item #1 Total Proposal:	\$ -8,023.05	292.05
		\$ 6,133.05



This should have been included in base bid and included in civil plans  
(Per Kris's email on 12-06-17)  
We show pavement removals and replacement based on what we know about existing utilities. GC is required to verify and bring up any discrepancies

CONTRACTOR: Ethan Giese Brickl Bros., Inc. Date: 12-1-17

$760 \text{ sq ft} \times \$6,133.05 \times .42 = 2,575.88$   
 $1026 \text{ sq ft} \times \$6,133.05 \times .58 \times .50 = 1,778.58$   
 revised. **\$ 4,354.46** Put this 2/9/18

**APPROVED AMOUNT**  
GPK 02-12-18

SECTION

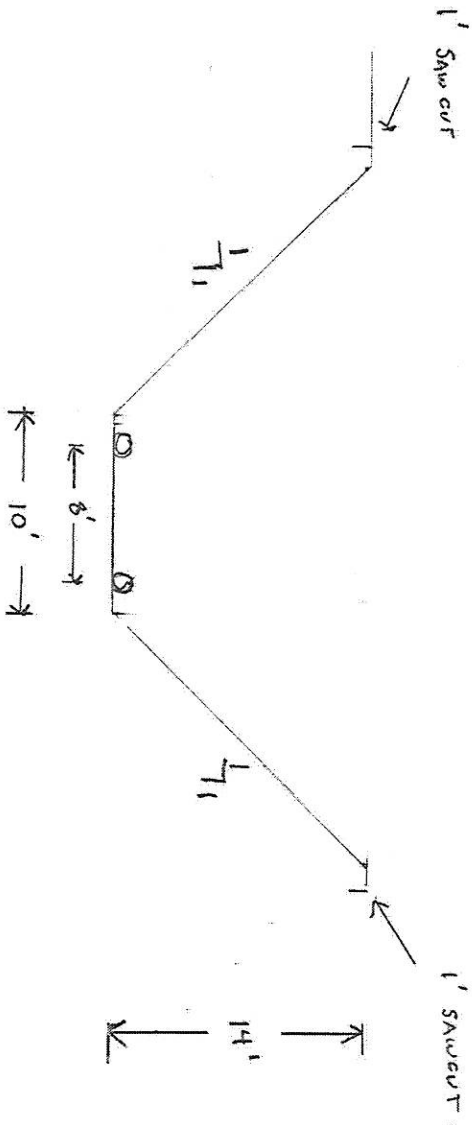

38'	EXTRA PATCH	513 sq	ACTUAL AREA IMPACT	3809	AREA SHOWN ON PLAN	7609	ACTUAL AREA IMPACT	3809	EXTRA PATCH	513 sq
-----	-------------	--------	--------------------	------	--------------------	------	--------------------	------	-------------	--------

PLAN VIEW



**Kozelek, Greg**

---

**From:** Ryan Welke <Ryan.Welke@is-grp.com>  
**Sent:** Monday, February 12, 2018 11:09 AM  
**To:** Kozelek, Greg  
**Subject:** RE: La Crosse Storage Facility - PR's

\*\*\* CAUTION: This email originated from an external sender. DO NOT click links or open attachments unless you recognize the sender and know the content is safe. \*\*\*

Greg,

The final cost they are requesting is \$4,354.46.

Thank you,  
Ryan

---

**From:** Kozelek, Greg [mailto:Kozelekg@cityoflacrosse.org]  
**Sent:** Monday, February 12, 2018 10:42 AM  
**To:** Ryan Welke <Ryan.Welke@is-grp.com>  
**Subject:** RE: La Crosse Storage Facility - PR's

Ryan:

Which cost is their final request?

Greg

---

**From:** Ryan Welke [mailto:Ryan.Welke@is-grp.com]  
**Sent:** Monday, February 12, 2018 9:32 AM  
**To:** Kozelek, Greg  
**Cc:** Nick Ellenberger  
**Subject:** RE: La Crosse Storage Facility - PR's

\*\*\* CAUTION: This email originated from an external sender. DO NOT click links or open attachments unless you recognize the sender and know the content is safe. \*\*\*

Good Morning Greg,

On our plan we called out an estimated 20' of pavement removal for utility installs but due to the depth of the water (14' rather than the typical 7') the excavator removed an additional 20' of pavement to achieve a 1:1 trench slope during excavation. Brickl stated that when they tore up the additional 20', the adjacent pavement was breaking up and they removed another 27' to create a clean edge and get back to solid pavement. Because the need for additional pavement was not made aware to ISG or City prior to or during the work, we feel it is fair to pay 100% for the additional 20' of paving required for excavation and 50% of the 27' of additional pavement removed to create a clean edge. Let us know if you need any additional information or have any additional questions.

Thank you,  
Ryan

---

**From:** Kozelek, Greg [<mailto:Kozelekg@cityoflacrosse.org>]  
**Sent:** Monday, February 12, 2018 8:51 AM  
**To:** Ryan Welke <[Ryan.Welke@is-grp.com](mailto:Ryan.Welke@is-grp.com)>  
**Subject:** RE: La Crosse Storage Facility - PR's

Ryan:

Can you tell me why we need to pay additional to replace the pavement in Green Bay Street ?

Thanks

Greg

---

**From:** Ryan Welke [<mailto:Ryan.Welke@is-grp.com>]  
**Sent:** Friday, February 9, 2018 3:57 PM  
**To:** Kozelek, Greg  
**Cc:** Nick Ellenberger  
**Subject:** RE: La Crosse Storage Facility - PR's

\*\*\* CAUTION: This email originated from an external sender. DO NOT click links or open attachments unless you recognize the sender and know the content is safe. \*\*\*

Good Afternoon Greg,

To follow up with my voicemail this week, we have wrapped up the review/ approval of the remaining PR's. Please see attached for the last additions to change order #5. (Pat did not have access to the documents that Ethan created these PR's from, that is the reason for the hand written revisions) Brickl is preparing the final pay app and we will submit as soon as it is received.

Let us know if you have any additional question/ comments.

Thank you,  
Ryan

**Ryan Welke - Certified Revit Professional**  
Project Coordinator

101 S. Reid Street, Suite 202  
Sioux Falls, SD 57103  
P: 605.274.6401  
C: 715.226.0910  
[ryan.welke@is-grp.com](mailto:ryan.welke@is-grp.com)



**Architecture  
Engineering  
Environmental  
Planning**



---

**From:** Kozelek, Greg [<mailto:Kozelekg@cityoflacrosse.org>]  
**Sent:** Monday, February 05, 2018 12:08 PM  
**To:** Ryan Welke <[Ryan.Welke@is-grp.com](mailto:Ryan.Welke@is-grp.com)>  
**Subject:** RE: La Crosse Storage Facility - PR's

Ryan:

Please review C O 5 and let me know if there are any additions.

Thanks

Greg

---

**From:** Ryan Welke [<mailto:Ryan.Welke@is-grp.com>]

**Sent:** Friday, February 2, 2018 2:36 PM

**To:** Kozelek, Greg

**Cc:** Nick Ellenberger

**Subject:** RE: La Crosse Storage Facility - PR's

\*\*\* CAUTION: This email originated from an external sender. DO NOT click links or open attachments unless you recognize the sender and know the content is safe. \*\*\*

Greg,

Thank you for the follow up. I have made Brickl aware of the February 23 but hopefully we can receive the rest of the closeout information next week from Brickl.

Thank you,  
Ryan

---

**From:** Kozelek, Greg [<mailto:Kozelekg@cityoflacrosse.org>]

**Sent:** Friday, February 02, 2018 10:54 AM

**To:** Ryan Welke <[Ryan.Welke@is-grp.com](mailto:Ryan.Welke@is-grp.com)>

**Cc:** Nick Ellenberger <[nick.ellenberger@is-grp.com](mailto:nick.ellenberger@is-grp.com)>

**Subject:** RE: La Crosse Storage Facility - PR's

Ryan:

Please pass the last P R s to me.

Pay requests were due last week so the next payment will be in March.

Please have all the documents to be before Feb 23.

Thanks

Greg

---

**From:** Ryan Welke [<mailto:Ryan.Welke@is-grp.com>]

**Sent:** Friday, February 2, 2018 9:44 AM

**To:** Kozelek, Greg

**Cc:** Nick Ellenberger

**Subject:** La Crosse Storage Facility - PR's

\*\*\* CAUTION: This email originated from an external sender. DO NOT click links or open attachments unless you recognize the sender and know the content is safe. \*\*\*

Good Morning Greg,

We have reviewed the final PR's for the La Crosse Storage facility, please see below for the list that we think are acceptable to approve. FYI... We received a call on Wednesday that Ethan Giese is no longer with Brickl and our point of contact to finalize this project will be Patrick Reis. ([pries@bricklbros.com](mailto:pries@bricklbros.com))

Let us know if you have any additional questions/ comments.

PR# 13 – We added rebar to the exterior approach slab.

PR #20 – This was for the additional paving in the parking lot to redo the entire lot requested by the Fire Department.

PR #23 – This is to paint the additional door added in PR #02 and has been confirmed that this was not included in the original PR when the door was added.

PR #27 – This was the additional cost to move the hot water heater (per the fire departments request during our initial punch list walk through) to give the Fire Department additional room for their gear washer.

PR #29 – We added a cove base in the shower area to protect the joint from water between the CMU and concrete floor.

PR #30 – The Fire Department requested Brickl to add two Bollards to protect the existing propane tank. We will include the paving as part of the retainage when Mathy comes back in the spring to patch around the added bollards.

PR #31 – This is a credit for Brickl not painting the Fire Suppression piping.

We still have a couple PR's outstanding that we have requested additional information from Brickl to complete our review and will be coordinating with them to finalize the final Pay App.

Thank you again for your assistance on this project.

Thank you,  
Ryan

**Ryan Welke - Certified Revit Professional**  
Project Coordinator  
Architecture Group



**Architecture  
Engineering  
Environmental  
Planning**

101 S. Reid Street, Suite 202  
Sioux Falls, SD 57103  
P: 605.274.6401  
C: 715.226.0910  
[ryan.welke@is-grp.com](mailto:ryan.welke@is-grp.com)





**Proposal Request 13**

Project: La Crosse Fire Department Storage Facility

Owner: City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

The following is a proposal for changes regarding PR 13:

	Proposal
Item #1: Labor and material for the addition of #4 Rebar at 2'-0" each way in the Concrete Approach Slab.	
Brickl Bros., Inc.	\$ 583.00
Subcontractor Markup:	\$ -
Item #1 Total Proposal:	\$ 583.00


CONTRACTOR:

  
Ethan Giese

Brickl Bros., Inc.

12-1-17

Date



**Proposal Request 20**

Project: La Crosse Fire Department Storage Facility


Owner: City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

The following is a proposal for changes regarding PR 20:

Item #1: Additional parking lot bituminous removal, grading & paving	Proposal
Brickl Bros., Inc.	\$ 13,000.00
Subcontractor Markup:	\$ -
Item #1 Total Proposal:	\$ 13,000.00

CONTRACTOR:

  
Ethan Giese

Brickl Bros., Inc.

12-1-17  
Date



**Back-Up: PR 22**  
**Project: La Crosse Fire Department Storage Facility**  
**Job #: 7605**  
**Date: 11-16-17**

**Item 1: PR 16**

**Division: 03**

Description: Engineering and installation of an additional 385 L.F. of Control Joints added to the Interior Slab on Grade, from revised Plan Sheet S1-12 and Pre-Pour Meeting.

Labor: ~~\$858~~ **\$353<sup>00</sup>** *PR. 2/7/18*  
Equipment: \$0  
Material: \$0  
Markup (10%): ~~\$85.80~~ **\$39<sup>00</sup>** *PR. 2/7/18*

Brickl Bros. Inc, proposes to furnish materials, labor and equipment in accordance with the above specifications, for the sum of:

~~\$943.80~~ **\$392<sup>00</sup>** *PR. 2/7/18*

Nine Hundred Forty-Three and 80 /100 Dollars

Authorized Signature: \_\_\_\_\_

*Eth Giese*  
Ethan Giese-Project Supervisor

Date: 11-18-17

*Eth Giese*

*2/7/18*



**Proposal Request 22 -REVISED 2/7/18**

Project: La Crosse Fire Department Storage Facility

Owner: City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

*160 LF  
O.K. P.R. 2/7/18*

We only added 2 control joints  
approximately 160 LF

The following is a proposal for changes regarding PR 22:

Item #1: Additional cost associated with Engineering and installation of an additional <del>365</del> <i>160</i> L.F. of Control Joints added to the Interior Slab on Grade, from revised Plan Sheet S1-12 and Pre-Pour Meeting.	Proposal
Brickl Bros.	\$ 943.80
Subcontractor Markup:	-
Item #1 Total Proposal:	<del>\$ 943.80</del>

Pricing to be updated with corrected per the updated LF

*\$392.00 PR 1*

CONTRACTOR:

*[Signature]*  
Ethan Giese

Brickl Bros., Inc.


*11-18-17*

Date

*[Signature]*

*2/7/18*





**Proposal Request 23**

Project: La Crosse Fire Department Storage Facility

Owner: City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

The following is a proposal for changes regarding PR 23:

Item #1: Paint Interior Shower Room Fiberglass Door & Fiberglass Frame 102A white.	Proposal
Pine Valley Painting	\$ 200.00
Subcontractor Markup:	\$ 10.00
Item #1 Total Proposal:	\$ 210.00

CONTRACTOR:

Ethan Giese

Brickl Bros., Inc.

12-6-17

Date



**Proposal Request 26** - *REVISED 2/7/18*

**Project:** La Crosse Fire Department Storage Facility

**Owner:** City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

*160 LF O.K.  
P.R. 2/7/18*

**Contractor:** Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669


*We only added 2 control joints  
approximately 160 LF*

The following is a proposal for changes regarding PR 26:

Item #1: Additional caulking for the <del>385</del> LF of added Control Joints required for the Interior SOG per the Architect.	Proposal
Beinborn Painting LLC	\$ <del>962.50</del>
Subcontractor Markup:	\$ 48.13
Item #1 Total Proposal:	\$ <del>1,010.63</del>

*400<sup>00</sup> P.A.  
20<sup>00</sup> P.A.  
\$420<sup>00</sup> P.A.*

*Pricing to be updated with  
corrected per the updated LF*

**CONTRACTOR:**  *12/21/2017*  
Ethan Giese Brickl Bros., Inc. Date  
*Eth G* *2/7/18*



**Proposal Request 27**

Project: La Crosse Fire Department Storage Facility

Owner: City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

The following is a proposal for changes regarding PR 27:

Item #1: Costs for additional piping required for the relocation of the hot water heater, per the Owner's direction.	Proposal
7Rivers Mechanical, LLC	\$ 567.22
Subcontractor Markup:	\$ 28.36
Item #1 Total Proposal:	\$ 595.58

CONTRACTOR:

Ethan Giese

Brickl Bros., Inc.

12/28/2017

Date


**7 RIVERS MECHANICAL LLC**

**MOVE FIRE STORAGE WATER HEATER**

Material Total	\$	149.45	
Fixture Total	\$	-	
Site Mat	\$	-	
DEMO MAT	\$	-	
Use Tax	\$	-	
Mat Labor	\$	281.05	3.85
Site Labor	\$	-	0
Fix Labor	\$	-	0
DEMO LABOR	\$	-	0
PERMIT	\$	-	0 Hours
NOT USED	\$	-	
Excavator	\$	-	
Insulator	\$	80.00	0 10' at 8.00 per foot
Blacktop rep	\$	-	
ADDED HRS	\$	-	0
TRAVEL	\$	-	
PROFIT	\$	56.72	4
	\$	567.22	
Perf bond	\$	-	
Total Bid	\$	567.22	

Tax Rate		0
Labor Rate	\$	73.00
Mark Up		10.00%

COST FOR MOVING THE WATER HEATER PER OWNER DIRECTION AT THE FIRE STORAGE.  
 INCLUDES 8' OF STUT, HANGERS, GAS PIPE AND FITTINGS, 4' IN TWO DIRECTIONS  
 OF 1 1/2" COPI



**Proposal Request 29**

**Project:** La Crosse Fire Department Storage Facility

**Owner:** City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

**Contractor:** Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

The following is a proposal for changes regarding PR 29:

Item #1: Changes to the Shower Room Base Finish to have an angled finish, instead of the 90 degree finish, per Owner direction.	Proposal
Midwest Tileworks	\$ 175.00
Subcontractor Markup:	\$ 8.75
Item #1 Total Proposal:	\$ 183.75

CONTRACTOR:

Ethan Giese

Brickl Bros., Inc.

12-28-2017

Date



**Proposal Request 30**


Project: La Crosse Fire Department Storage Facility

Owner: City of La Crosse Fire Department  
 2300 Green Bay St.  
 La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
 400 Brickl Road, PO Box 125  
 West Salem, WI 54669

The following is a proposal for changes regarding PR 30:

		Proposal
Item #1: Installation of (2) painted pipe bollards per direction from the Owner on the East Side of the newly paved Parking Lot to protect the Existing Propane Tank. Note: the patching of the Asphalt done by Mathy is to be done in the Spring when the temperatures allow of this work to be done.		
Payment in the spring	→ Pine Valley Painting	\$ 100.00
	Mathy Paving	\$ 600.00
	Brickl Bros.	\$ 884.40
Subcontractor Markup:		\$ 35.00
Item #1 Total Proposal:		\$ 1,619.40

CONTRACTOR:  12/21/2017  
 Ethan Giese                      Brickl Bros., Inc.                      Date



**Back-Up: PR #30**  
**Project: La Crosse Fire Department Storage Facility**  
**Job #: 7605**  
**Date: 12-21-17**

**Item 1: PR #30**

**Division: 03**

---

**Description: Labor and material to install (2) Pipe Bollards to protect the Existing Propane Tank on the East Side of the Parking Lot.**

Labor: \$528  
Material: \$276  
Markup (10%): \$80.40

Brickl Bros. Inc, proposes to furnish materials, labor and equipment in accordance with the above specifications, for the sum of:

\$884.40  
Eight Hundred Eighty-Four and 40/100 Dollars

Authorized Signature: \_\_\_\_\_

Ethan Giese-Project Supervisor

Date: 12/21/2017



**Proposal Request 31**

Project: La Crosse Fire Department Storage Facility

Owner: City of La Crosse Fire Department  
2300 Green Bay St.  
La Crosse, WI 54601

Contractor: Brickl Bros., Inc.  
400 Brickl Road, PO Box 125  
West Salem, WI 54669

The following is a proposal for changes regarding PR 31:

Item #1: Credit for not painting the Fire Suppression piping.	Proposal
Pine Valley Painting	\$ (800.00)
<hr/>	
Subcontractor Markup:	
Item #1 Total Proposal:	\$ (800.00)

CONTRACTOR: \_\_\_\_\_  
Ethan Giese                      Brickl Bros., Inc.                      Date
