



BVisions Media Image-War Eagle, February, 2026

River Point District

Project Management Report-March, 2026

JBG Planning LLC

Contents

Project Management Update-March, 2026

Section 1.

A. Monthly activity summary divided into categories; public infrastructure, investor/developer activity, partnerships activity, financial highlights, design or PDD reviews

Section 2.

- A. Analysis of challenges and opportunities narrative
- B. Future/existing potential funding solutions and strategies
- C. Partnership solutions and strategies
- D. Ongoing investor/developer contacts/communications
- E. Public/media relations and communications updates
- F. Map panel showing investor activity and Architectural Imagery

Section 3.

A. Map Panels showing future infrastructure phasing and project schedules and plat

Section 4.

A. Contacts for Residents and Developers

Section 5.

A. 2025 Year End Report

Monthly Activity Summary

Investor/developer activity

Since last RDA Meeting:

1. Coordination with developers on RFEI response and schedule for lots 11, 12, 1 and 2
2. Coordination with RyKey on Major Employer contacts-Newly released information from the La Crosse Chamber
3. Coordination with 360 Real Estate on 2025-2026 Schedule and acquisitions
4. Coordination on commercial tenant prospects with developers-communications with Red Earth
5. Coordination on Renter Equity programs and LCF Grant (Grant Awarded) , meetings with housing agencies, financial management firms, employers
6. Contact with Unwind Property Management lots 1 and 2
7. Coordination with MSP on March presentation for lot 6
8. Assistance with land assembly and acquisitions Kraft Street
9. Engaged UW Department and student on health performance metrics and impending study-phase two underway

Option Agreement status:

RyKey Lot 8 Sold

RyKey: -Extension approved for Lot 9 Gateway Commons for 12 months to July, 2025-Extension Granted for 12 months to July, 2026.

360: April 27-April 27, 2024 (12 months)-Approved a 12 month extension to August, 2025-Option Extension granted for 9 months to May, 2026.

Lot 6 Option-Draft complete for MSP-Option for 6 months executed

MSP, Sold and Completed (Ribbon Cutting Spring of 2025)

Red Earth/War Eagle: Closed and under construction

Red Earth, Lots 3 and 4 and 5: 12 month extension approved to September 26, 2025-On Hold

RyKey, Lot 11 Awarded, Lot 12 Pending Signatures

Lots 1 and 2 Pending Approval, March 2026 RDA Meeting

Partnership Activity

JBG Planning LLC has met with the following stakeholders:

- Fielding inquiries from interested investors and future residents-missing middle housing
- Field progress photography and coordination on BVisions Videography Project
- Energy systems coordination for possible joint parkway-development use
- Telephone Inquiries from developer/investors and prospective residents
- Ongoing communications with new investor on RFEI land opportunities
- Updating Smartsheet database on construction schedule
- LCF Grant Award Coordination and update with Community Foundation staff
- ULI Spring Meeting coordination

Project Challenges and Opportunities

Analysis of challenges and opportunities narrative

Challenges:

1. Review with City Engineering/Public Works the implications of infrastructure ownership by the Redevelopment Authority short and long term
2. Unclassified excavation (contaminated soil) is always a potential cost challenge. Soil disposal costs \$75/cy at the La Crosse County Landfill. (Depending on concentration) and organics affecting the costs of footings/piers. Concrete monolith meeting with Braun Intertec.-Also concrete monolith issues
3. Anticipate the investment in the relocation and costs of the large electrical distribution line along the Black River frontage.
4. TIF application review and needs relative to city policy
5. Timing of projects given external factors such as financial, agency/environmental and supply chain issues including national economic policy impacts
6. Long Term Landscape Maintenance-Contract Complete
7. Construction inflation, tariff impacts, interest rates, external economic factors, financial structures.
8. Lot 12 Concrete Monolith

Opportunities:

9. Continue to market the development opportunities -RFEI issued and developer communications underway
10. Costs of parks/recreation improvements should be coordinated with grant application opportunities
11. La Crosse Community Foundation Social Investment Interests, Renter Equity Grant
12. Potential for renter equity programs and partnerships
13. Ground or building lease opportunities for RDA (to be discussed on case by case basis)
14. Public Private partnerships for Public Parking and/or programmable interior/exterior community spaces
15. Marina partners/leases
16. Discuss maintenance strategies to keep RPD looking good and possible future NID transition-Possible tie to the marina/slips maintenance program
17. Neighborhood Improvement District
18. Lot 12 creative use of real estate

Future/existing potential funding solutions and strategies. See

Smartsheet Funding Resource. Note: As the project is further evaluated, specific funding sources from this resource will be identified and pursued at the discretion of the RDA. Parks and Recreation improvements are a great candidate for third party funding.

Ongoing investor/developer contacts/communications


Meetings with both currently engaged investors and prospective investors are underway by JBG Planning LLC. Since some of these meetings involved RDA negotiations, communications on these meetings will need to be handled in closed session.

Public/media relations and communications updates

JBG Planning LLC is working with the City's PIO to address media inquiries and update media, which will include an immediate release section in each RDA report.

Investment Phases Map

Anticipated Private Investment Based on Current Option Agreements

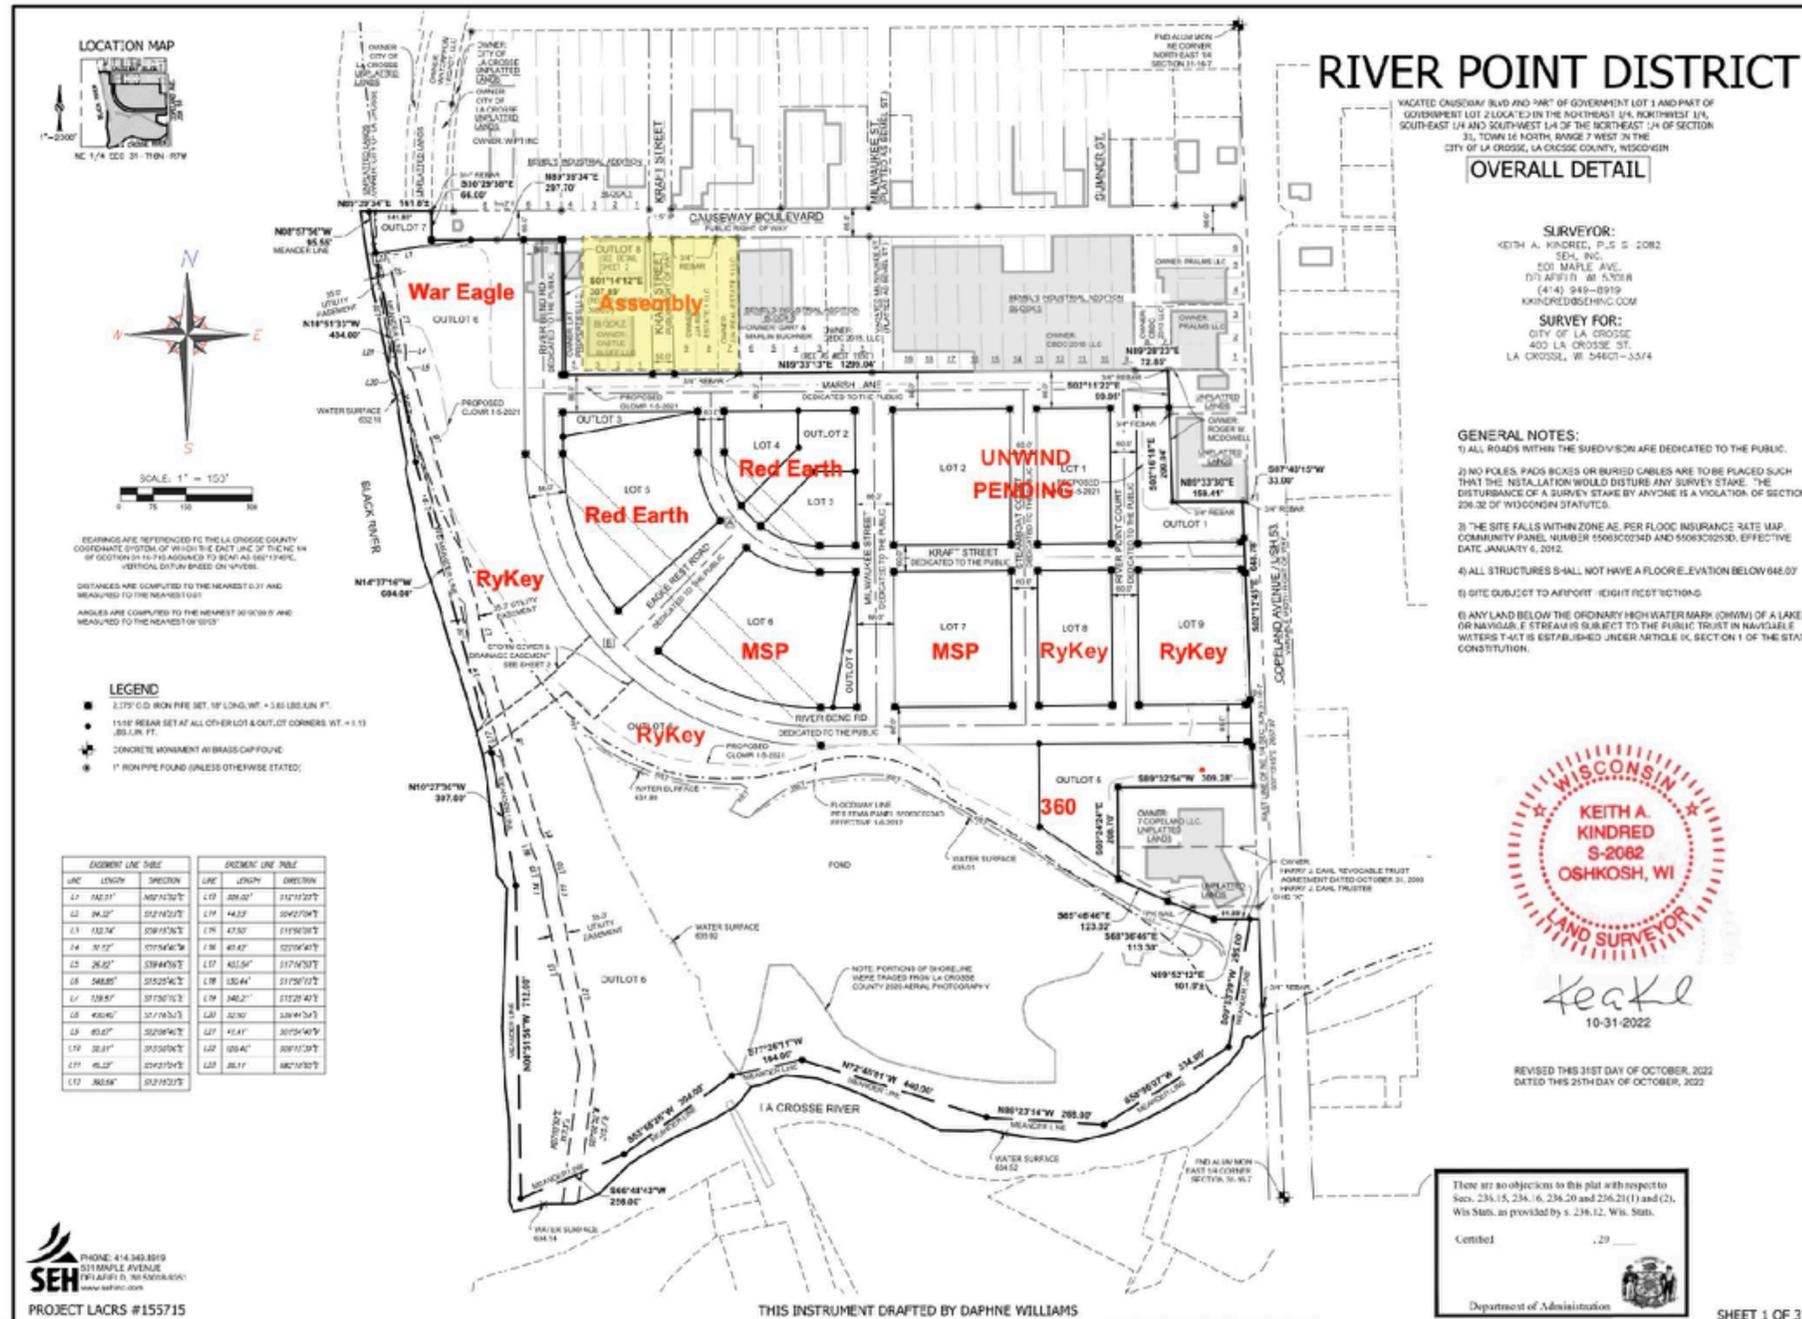

Option Agreement status:

RyKey Lot 8 Sold

RyKey: -Extension approved for Lot 9 Gateway Commons for 12 months to July, 2025-Extension Granted for 12 months to July, 2026.

360: April 27-April 27, 2024 (12 months)-Approved a 12 month extension to August, 2025-Option Extension granted for 9 months to **May, 2026.**

Lot 6 Option -MSP Option Pending
MSP, Sold and Completed (Ribbon Cutting Spring of 2025)

Red Earth/War Eagle: Closed and under construction


Red Earth, Lots 3 and 4 and 5: 12 month extension approved to September 26, 2025

Lots 1, 2, 11 and 12 RFEI Issued

Lot 11 awarded to RyKey-6 months to June, 2026

Lot 11 Pending

Investment Character Reference-Current Options

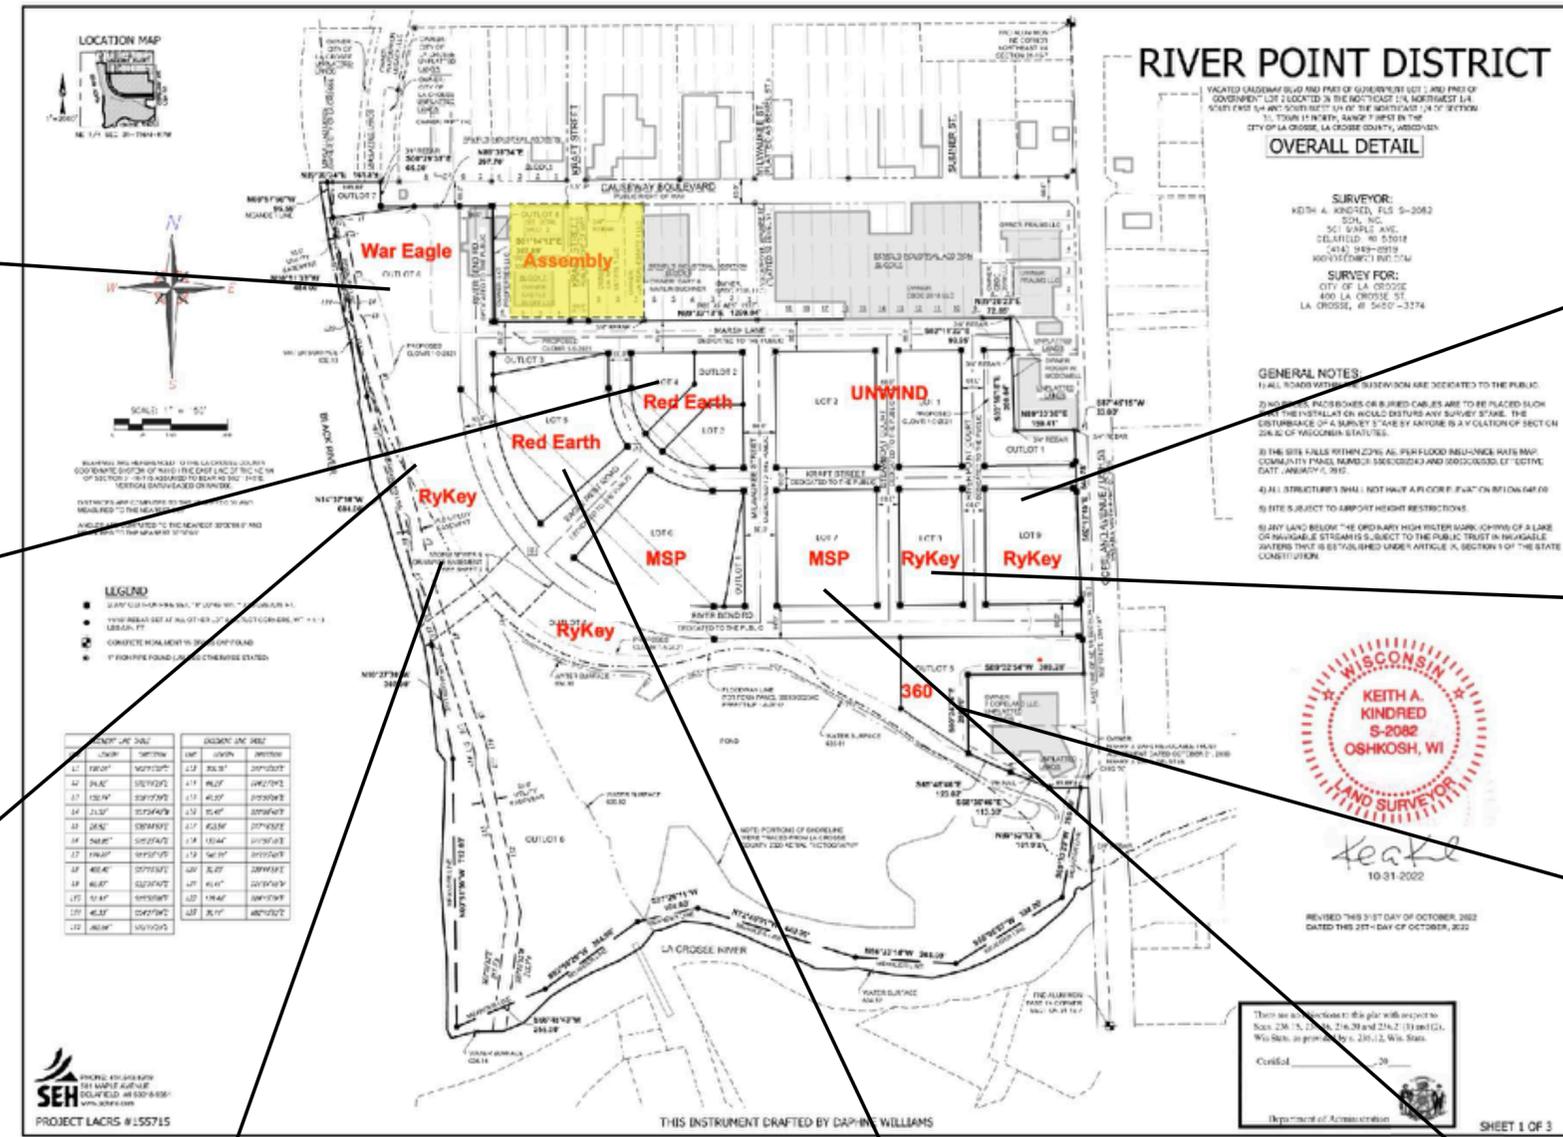

2026 Housing and Space Proposed

River Point District, 2026

Housing Proposed by Parcel

Lot 8, RyKey Development:

52-1 bdrm
4-2 bdrm
56 Units

Lot 1 and 2-Developer Proposals Pending

42 Townhomes

Lot 3 and Lot 4, Red Earth LLC

18 Townhouse Condominium Units
All 3 bdrm units

LOT 5, Red Earth LLC

206 UNITS
16-Studio
36-1 bdrm
8-1 bdrm + den
32-2 bdrm
8 3 bdrm

LOT 6-Option Signed with MSP

165-180 Units, 55 and older market rate
Mix Pending

LOT 7, MSP

- 68 1-BEDROOM UNITS
- 32 2-BEDROOM UNITS
- 100 UNITS TOTAL
TOWNHOUSES:
- 20 3-BEDROOM UNITS

Total: 120 UNITS TOTAL ON SITE.

LOT 9, RyKey Development

151 Units+ Commercial Space
123-1 bdrm and studio
20-2 bdrm
8-3 bdrm

LOT 10 War Eagle LLC

59 UNITS + 12K Commercial Space
22-1 Bdrm
6-1bdrm + den
11-2 bdrm
12-3bdrm

LOT 11 RyKey

Details Pending

LOT 12 RyKey

Details Pending

LOT 13 360 Real Estate

21 Units
21 studio units+ 12K Commercial Space

Outlot 5 360 Real Estate

92 Units
36 1 bdrm
28 2bdrm
28 Studio

Total Housing Units Proposed as of 01-2026

963 with more detail to come on Lots 11, 12, 1 and 2.

Commercial Space Proposed

While we have some preliminary numbers on the mixed use buildings, the square footages for commercial space are somewhat variable as developers negotiate with potential tenants for build-to-suit space

Project Metrics

Social, Environmental, Economic and Cultural Outcomes by Project

JBG Planning LLC has developed a tool to assist the RDA in its decision making process for both public and private investment within the development. This tool provides guidance on quantifying project impacts using social, environmental, economic and cultural metrics.

See the Smartsheet tool. Under the Direction of Andrea Trane, JBG Planning has currently engaged UW La Crosse in studying the health impacts/metrics of the River Point District Development.

Here are some examples of Metrics outlined by various developers proposing investment in River Point District:

1. How does the project relate to social investment in the City

The Merge River Point District development project meets several social sustainable performance indicators. The project will be a short walking distance of public parks, multiple greenspace areas, opportunities for water recreation, and will provide easy accessibility to the public recreation trail system. Throughout the River Point District bike lanes are included on the master plan which will serve as additional pathways to the above listed destinations. A designated tenant fitness area within the project which is currently a planned amenity. Lastly, the main level commercial space will allow for a multiple to socially beneficial businesses a place to operate.

2. How does the project achieve economic investment in the City

The Merge River Point District development project will increase the number of rentable units available to new and current residents of La Crosse. The project would have a direct positive effect on the jobs to housing ratio. Additionally, the ground floor commercial spaces will add locations for new or relocating businesses. The adding of jobs and housing will only benefit the future economic growth of La Crosse. Lastly, All Merge projects strive to provide high speed internet access to all tenants by partnering with local ISP providers.

3. How the project achieve environmental metrics in the City

All planned construction will meet and exceed minimum energy efficiency standards. Merge partners with 3rd pattern consultants to use Focus On Energy initiatives to ensure the highest level of building efficiencies. These upgrades in building insulation modeling, appliances, and mechanical systems all work cohesively to lower energy consumption and lower tenant utility costs. The development will incorporate mindful planning for stormwater runoff. Additional onsite detention and green spaces help alleviate the burden of added non-permeable surfaces. Adding new housing opportunities closer to residents' employment will allow for a reduction in greenhouse emissions.

4. Are there cultural offerings or metrics associated with the project?

The commercial space would be available to any and all potential businesses. These could include cultural focused companies that could provide additional services to the area.

For Immediate Release

BVisions Media Image



MSP-The Driftless, February, 2026



Appendix

PDD General Land Use Map-Newly Revised

2.0 SPECIFIC DEVELOPMENT PLAN

RIVER POINT DISTRICT

2.2 Land Use Diagram

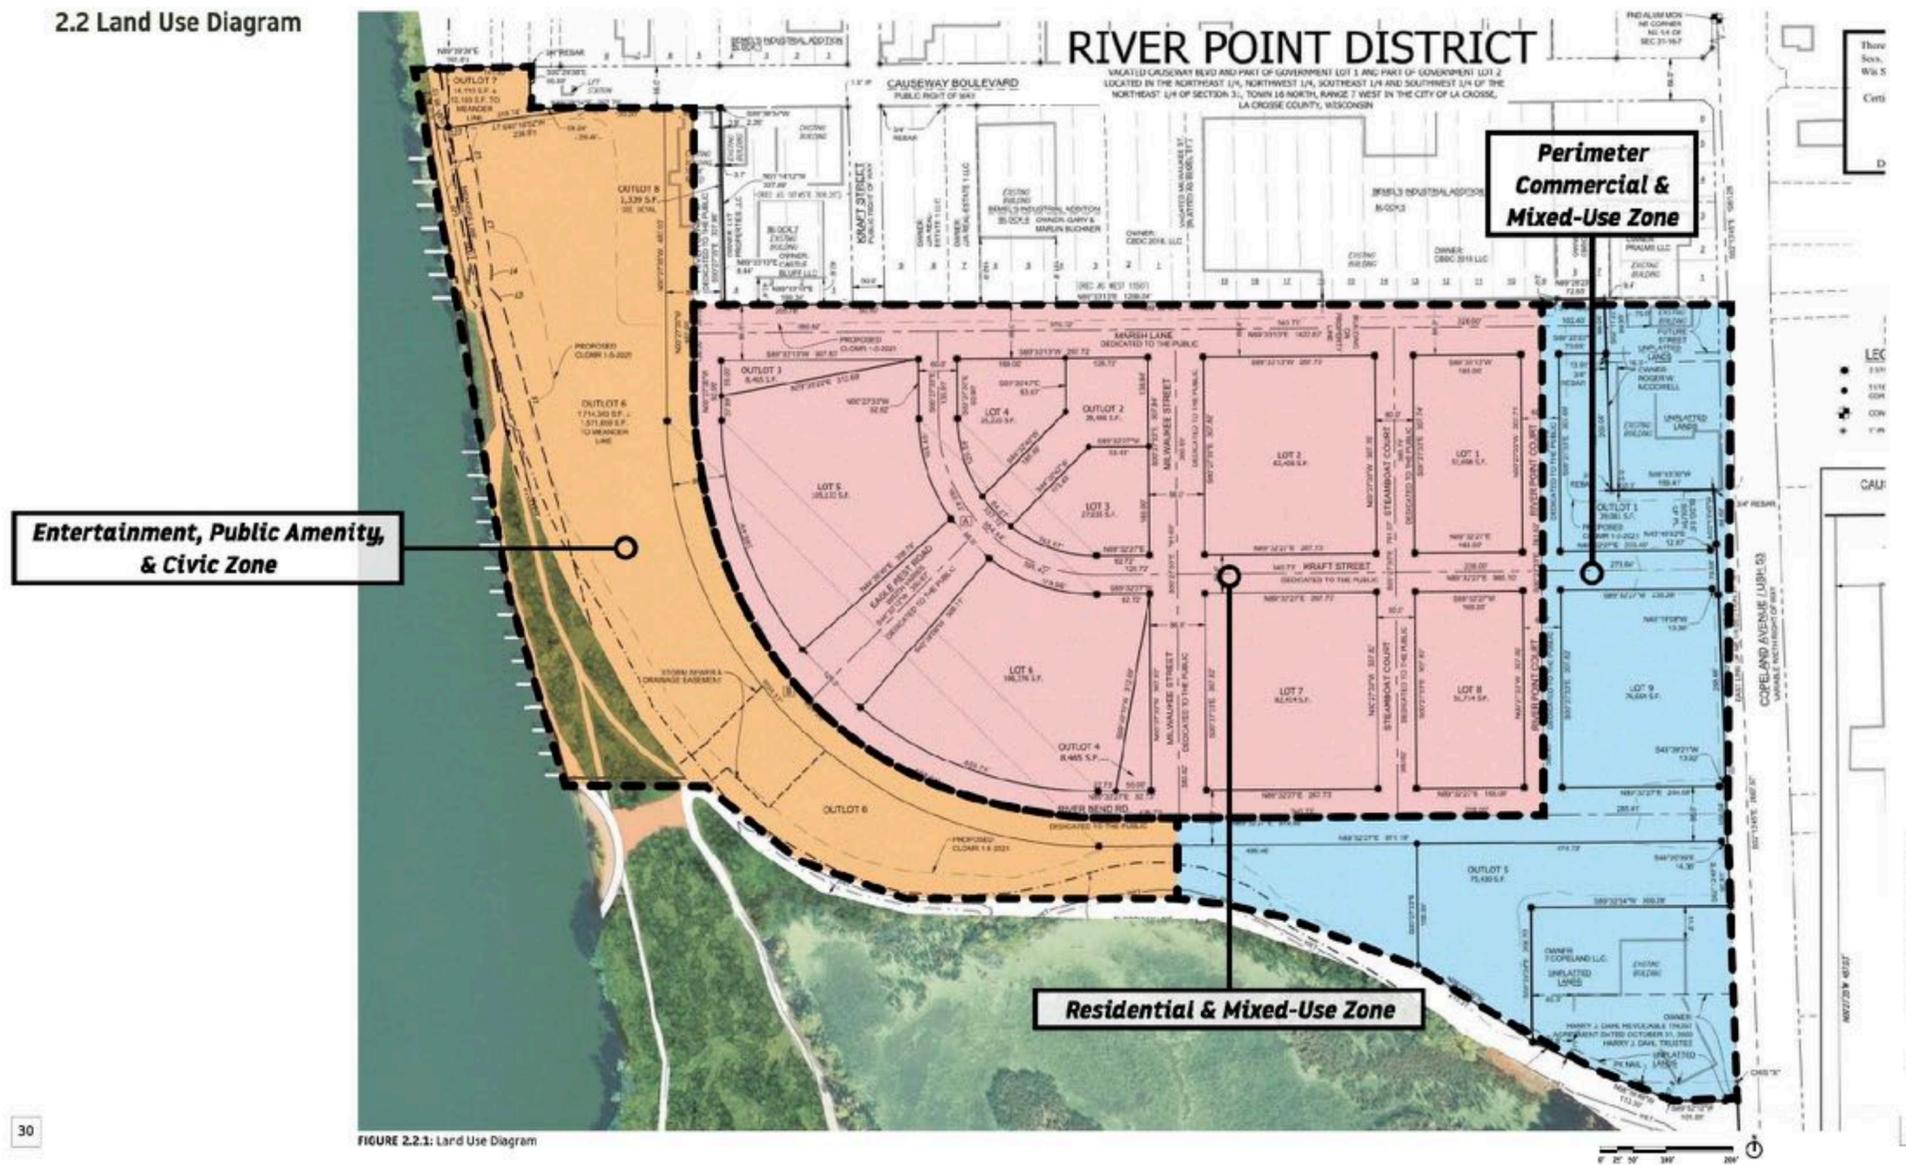


FIGURE 2.2.1: Land Use Diagram

Appendix

PDD General Land Use Map-Newly Revised

2.0 SPECIFIC DEVELOPMENT PLAN

RIVER POINT DISTRICT

2.3 Development Summary


The development summary below outlines the approximate lot sizes, possible parking estimates, and potential building uses based on the conceptual masterplan illustrated in this PDD document. The below table in no way limits the use or size of individual buildings within the masterplan.

TABLE 2.3.1: Development Summary

| Lot or Outlot | Approximate Square Footage | Approximate Acreage | Description |
|---|----------------------------|---------------------|--|
| ZONE A1 - Perimeter Commercial & Mixed-Use Zone | | | |
| OUTLOT 1 | 39,081 | 0.90 | Zone A1 allows for commercial/retail opportunities. Mixed use buildings with ground floor commercial/retail activation with residential floors above is favorable. Building height in Zone A1 shall be a minimum of 2 stories. |
| ZONE A2 - Perimeter Commercial & Mixed-Use Zone | | | |
| LOT 9 | 76654 | 1.75 | Zone A2 allows for commercial/retail opportunities. Mixed use buildings with ground floor commercial/retail activation with residential floors above is favorable. Building height in Zone A2 shall be a minimum of 2 stories. |
| ZONE B1 - Residential & Mixed Use Zone | | | |
| LOT 1 | 51,698 | 1.19 | |
| ZONE B2 - Residential & Mixed Use Zone | | | |
| LOT 8 | 51,714 | 1.19 | |
| ZONE C - Residential & Mixed Use Zone | | | |
| LOT 2 | 82405 | 1.89 | |
| ZONE D - Residential & Mixed Use Zone | | | |
| LOT 7 | 82414 | 1.89 | |
| ZONE E - Residential & Mixed Use Zone | | | |
| OUTLOT 2 | 28486 | 0.65 | |
| LOT 3 | 27035 | 0.62 | |
| LOT 4 | 26220 | 0.60 | |
| ZONE F - Residential & Mixed Use Zone | | | |
| LOT 6 | 106376 | 2.44 | |
| OUTLOT 4 | 8465 | 0.19 | |
| ZONE G - Residential & Mixed Use Zone | | | |
| LOT 5 | 105133 | 2.41 | |
| OUTLOT 3 | 8465 | 0.19 | |
| ZONE H - Entertainment, Public Amenity, & Civic Zone | | | |
| OUTLOT 6 | 1714343 | 39.36 | Entertainment, Public Amenity, & Civic. Mixed Use opportunities. Multi-family residential above retail. |
| OUTLOT 7 | 14110 | 0.32 | |
| ZONE J - Perimeter Commercial & Mixed-Use Zone | | | |
| OUTLOT 5 | 75430 | 1.73 | Zone J allows for commercial/retail opportunities. Mixed use buildings with ground floor commercial/retail activation with residential floors above is favorable. Building height in Zone J shall be a minimum of 2 stories. |
| TOTAL | | 57.35 | |

*Acreages shown do not include public roadways or public green spaces.

FIGURE 2.3.2: Site plan with labeled zones corresponding to the development summary.

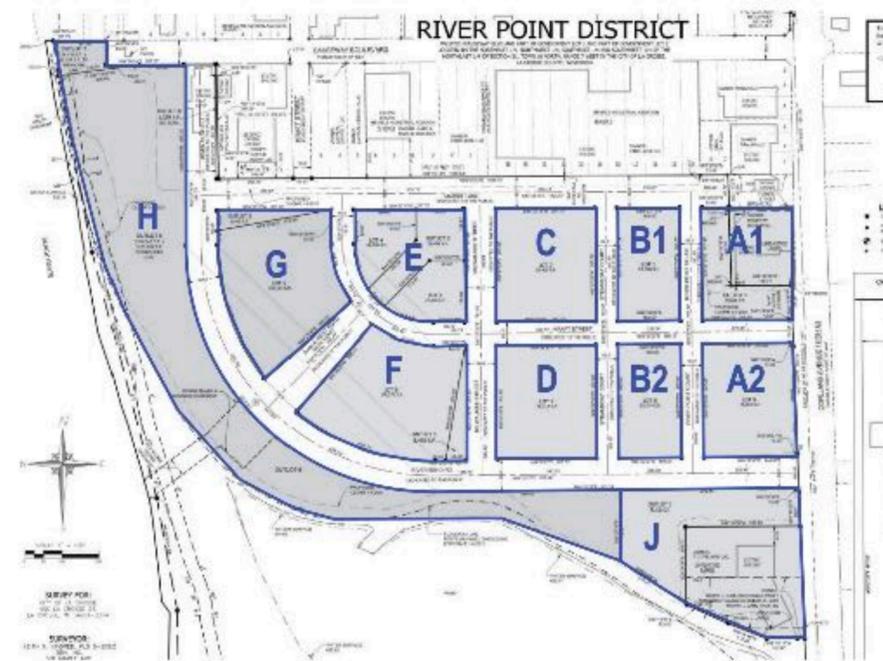

General Development Plan

2.0


Appendix

PDD Master Plan-Reference Parcel Map

FIGURE 2.3.1: Site plan with labeled zones corresponding to the development summary.



Appendix-Plat Lot Size Map

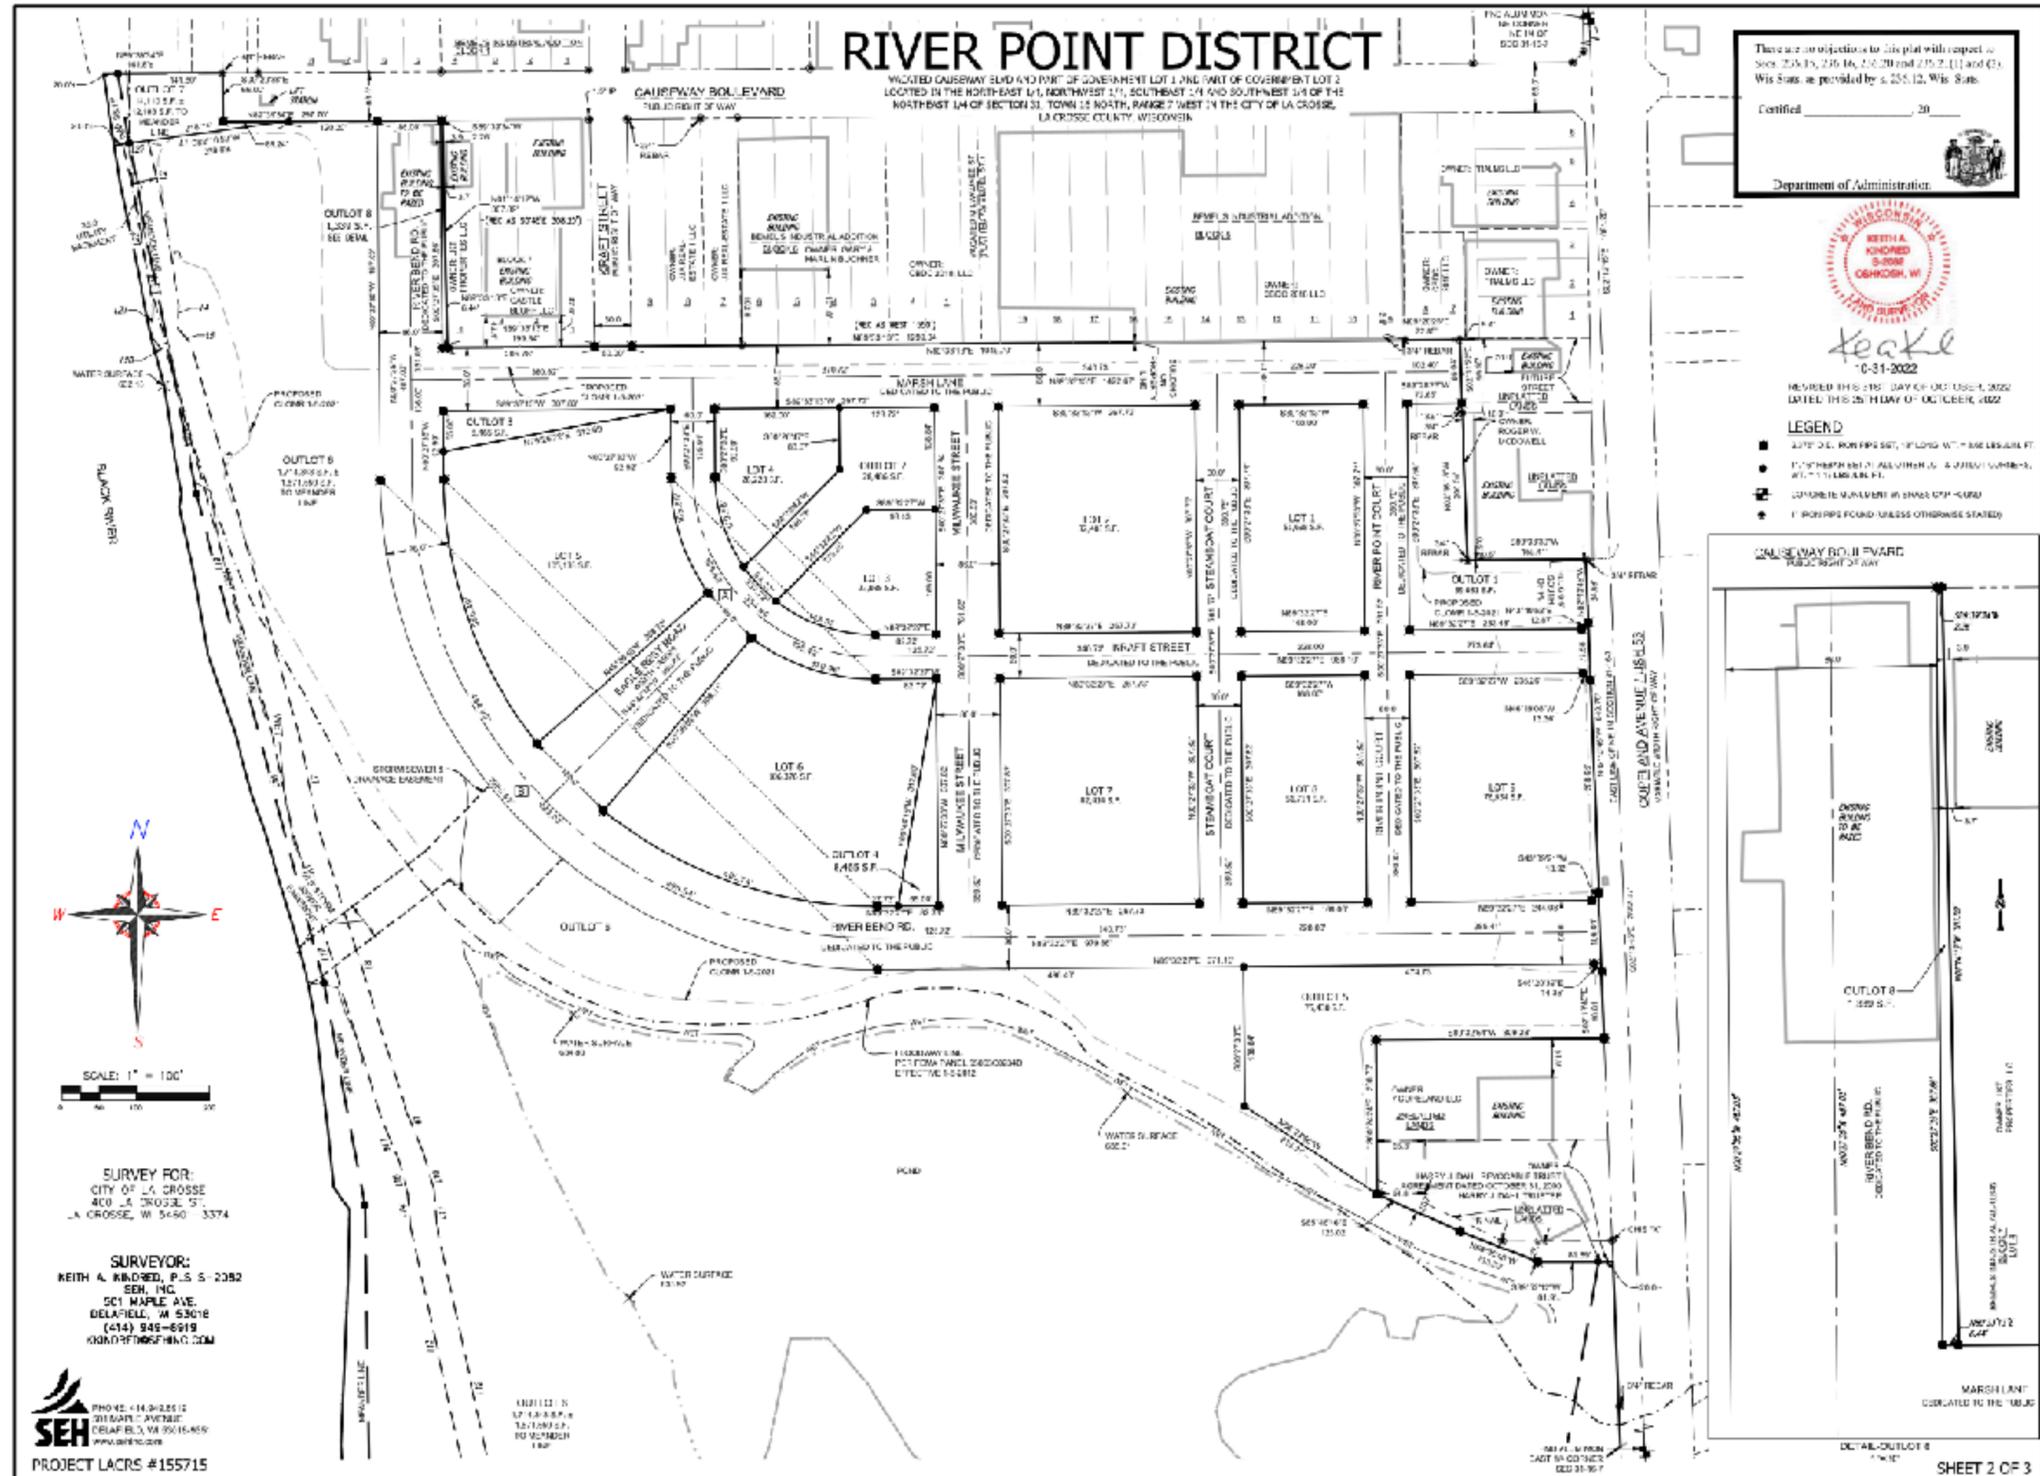

Appendix-Non Exclusive Option Language

Delay Termination. The RDA reserves the right to review proposals from other investors on parcel_____. Should a viable proposal be brought forward by another developer, the RDA may, in its discretion, inform the current option holder of the alternate proposal and at the time of the receipt of a complete alternate proposal, the RDA may require additional information and or guarantees from the current option holder based on the option holder's original proposal (RDA) illustrating the project is progressing to construction commencement as presented per the original presentation and subsequent updates by the developer to the RDA.

Should the option holder (developer), fail to provide an adequate guarantee of progress for the proposed development to the RDA, the RDA may terminate the option with a 30-day notice and return a prorated amount of the option fee to the developer.

Appendix-Leasing Agents

Information for the Driftless Apartments:
MSP

The Driftless

Tammy Ross, Regional Manager

323 River Bend Rd

La Crosse, WI 54603

P: (608) 292-8770

F: (715) 430-2462

thedriftless@msphousing.com

Information for the **War Eagle** development:

Red Earth: Lori Fuselier lori@3amigosapartments.com

Information for **RyKey's Lofts at River Point District** (next to the Driftless Apartments on Lot 8):

Jessica Magnusen: jessica@rykeyproperties.com

Year End Report for 2025

Option Agreements

- Lot 6 MSP
- Lot 12 RyKey
- Outlot 5-Lot 13 360

Land Assembly

- Kraft Street-Marsh Lane Assembly Underway

New Construction

- War Eagle-Lot 10 under construction and partial occupancy
- The Lofts-Lot 8 under construction -spring occupancy

Planning

- Marina and Parkway Planning progressing-grant research completed
- UW Student Engagement on public health impact of development-underway

Operations and Maintenance

- Snow Removal and Mowing contracts executed
- Ground Lease or NID under review

Grants

- La Crosse Community Foundation-Renter Stability Grant

Public Relations

- Website updates
- Fielded calls <100
- La Crosse Community Foundation Grant for Renter Equity
- Urban Land Institute Spring Conference Invitation
- Presentations to Downtown, Valley View Rotary, Chamber Leadership, LABA, Chancellor Tour
WXOW, APA State Conference, 7 Rivers Alliance, Habitat, CouleeCap
